



# ROAD BOND PROGRAM

## Construction Summary Report


County Judge  
Bill Gravell, Jr.

Commissioners  
Terry Cook  
Cynthia Long  
Valerie Covey  
Russ Boles

# August 2024

[WWW.WILCOTX.GOV](http://WWW.WILCOTX.GOV)

Volume XXIX - Issue No.8

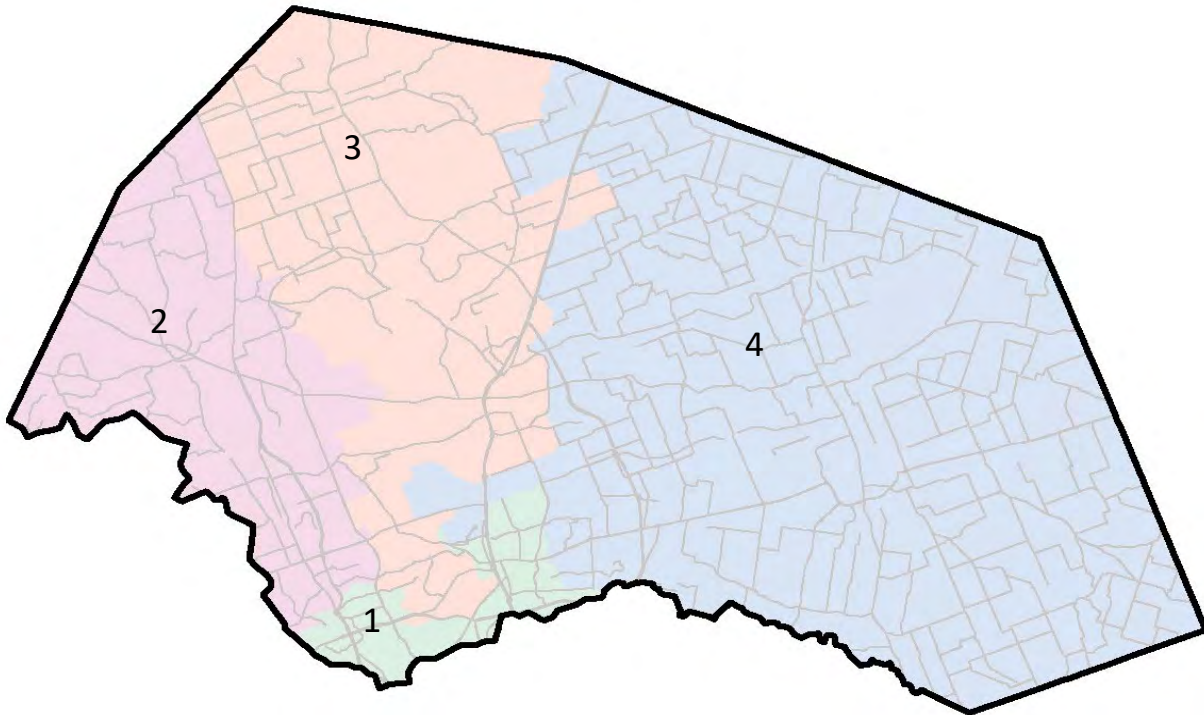

Presented By:



# Table of Contents



Completed Projects ..... 1

PRECINCT No. 1 – Commissioner Terry Cook..... 5

PRECINCT No. 2 – Commissioner Cynthia Long ..... 9

CR 258 Extension (US 183 to Sunset Ridge Drive)..... 13

Liberty Hill (SH 29) Bypass (RM 1869 to CR 279).....14

Ronald Reagan Boulevard Widening.....16

PRECINCT No. 3 – Commissioner Valerie Covey ..... 17

CR 111 Westinghouse Road ..... 21

CR 245 Reconstruction ..... 23

Corridor H/Sam Bass Road ..... 24

PRECINCT No. 4 – Commissioner Russ Boles..... 26

East Wilco Highway (Southeast Loop Segment 1, Phase 1) .....30

CR 401 Reconstruction..... 31

Samsung Highway (Future County Road) (CR 404 to FM 973)..... 33

East Wilco Highway (FM 3349 at US 79 (FM 3349 from US to CR 404))..... 34

CR 366 (Chandler Road to Carlos G. Parker Boulevard)..... 38

Bud Stockton Extension (CR 305 to FM 487)..... 40

CR 307 and CR 305 (CR 307 North of CR 305)..... 41

Corridor C / SH 29 Bypass ..... 42

CR 129 (South of Brushy Creek to North of South County Line).....44

CR 332 Realignment (South of FM 487 to North of CR 313).....46

CR 138 Right Turn Lane at SH 30.....47

Bud Stockton at FM 487 Traffic Signal .....48

# WILLIAMSON COUNTY


## ROAD BOND PROGRAM

### COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF AUGUST 2024

#### Precinct 1

- Pond Springs Road (signal) – Apr 2002
- McNeil Road, Phase 1 – Jan 2005
- McNeil Road, Phase 2 – Feb 2007
- RM 620, Phase 1 – Jan 2009
- Pond Springs Road – Sep 2010
- County Road 174 at Brushy Creek – Jun 2011
- O'Connor Drive Extension – Apr 2012
- King of Kings Crossing – Aug 2012
- RM 620 Safety Improvements – Dec 2014
- Forest North Drainage Improvements Phase 2 – Oct 2017
- O'Connor Drive N of RM 620 – Jul 2018
- Neenah Avenue Widening – Dec 2018
- Lakeline Right Turn Lanes – Aug 2019
- Forest North Drainage Improvements – Anderson Mill – Feb 2020
- North Mays Extension- Dec 2020
- Forest North Drainage Improvements Phase 3 – Jan 2022
- RM 620 at Railroad/Chisolm Trail – Dec 2023

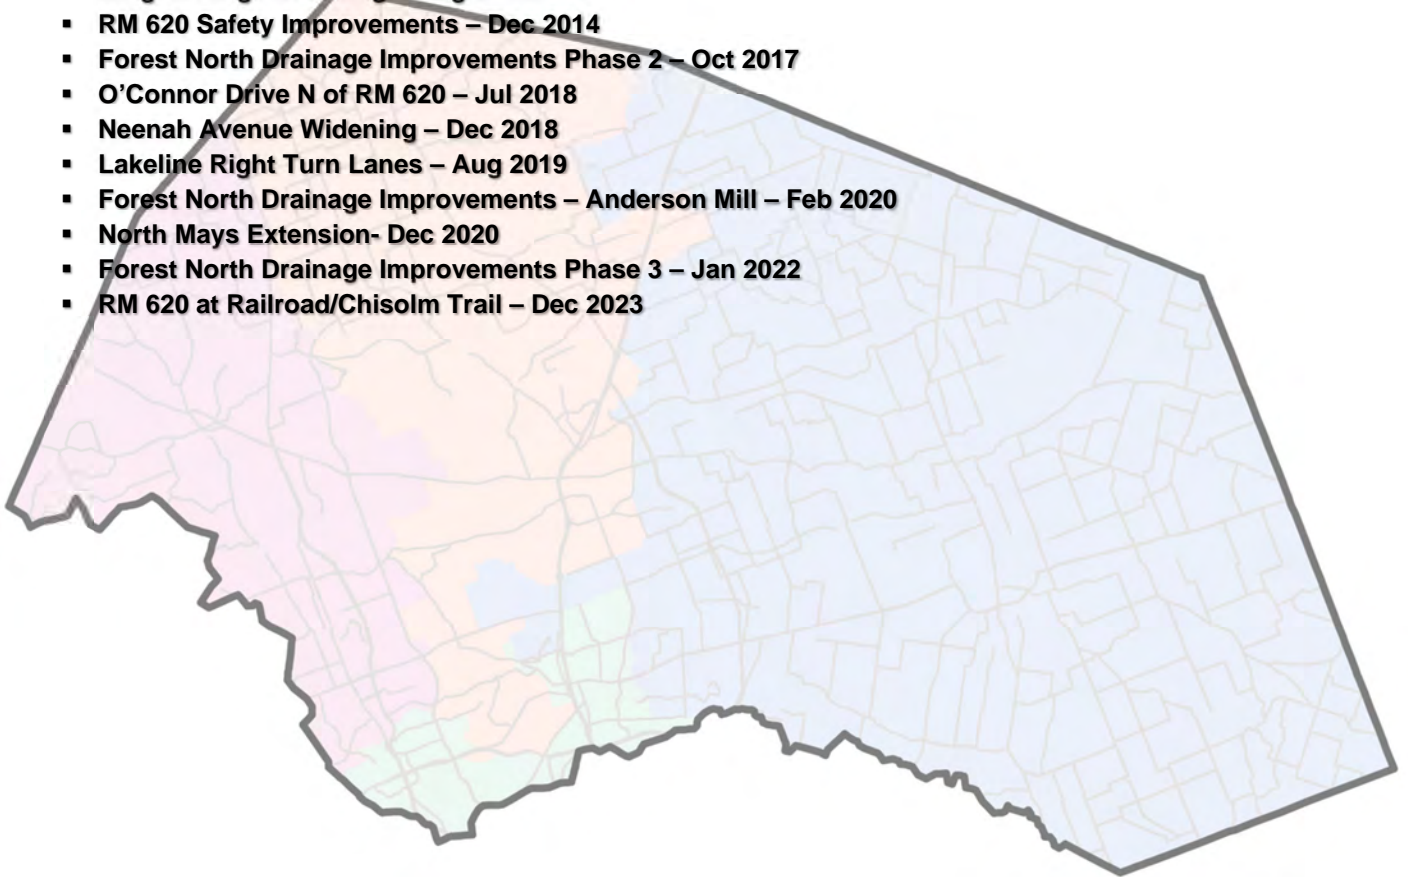

# WILLIAMSON COUNTY

## ROAD BOND PROGRAM

### COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF AUGUST 2024

#### Precinct 2

- RM 1869 at SH 29 (signal) – Aug 2002
- River Bend Oaks – Feb 2003
- County Road 175 – Jun 2003
- County Road 200 – Sep 2003
- Ronald Reagan Blvd, South Ph. 1 – Dec 2004
- County Road 214 – Feb 2005
- County Road 258 – Sep 2006
- San Gabriel Pkwy, Ph. 1 – Feb 2007
- Ronald Reagan Blvd North Ph. 1 – Mar 2007
- Lakeline Blvd – Jul 2007
- Ronald Reagan Blvd South Ph. 2 – Feb 2008
- US 183 at CR 274 – Feb 2008
- County Road 175 Phase 2A – Jan 2010
- US 183 at FM 3405 Traffic Signal – Mar 2010
- US 183 at FM 3405 Left Turn Lanes – May 2010
- County Road 214 Phase 2A – Jan 2011
- San Gabriel Parkway Ph. 2 – Oct 2011
- US 183 (PTF) – Apr 2012
- SH 29 TWLTL Liberty Hill – Dec 2012
- Hero Way – Feb 2013
- County Roads 260/266 – Apr 2013
- County Road 277 – Jul 2014
- Lakeline Blvd at US 183 – Nov 2014
- Lakeline Blvd Ph. 2 – Apr 2015
- County Road 258 – Jul 2017
- County Road 200 at Bold Sundown – Oct 2018
- Ronald Reagan at Santa Rita Ranch – Feb 2019
- CR 200 at SH 29 / Loop 332 – Jul 2019
- Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road) – Feb 2020
- San Gabriel Ranch Road Bridge – Mar 2020
- Corridor F / US 183 Planning - Jan 2021
- Seward Junction Improvements – Mar 2021
- Ronald Reagan Blvd Widening (Temporary Signals) at Santa Rita Blvd – Feb 2022
- CR 200 (CMTA Railroad to CR 201) – Oct 2022
- Ronald Reagan Safety Improvements – July 2023
- CR 258 Extension – Dec 2023




# WILLIAMSON COUNTY

## ROAD BOND PROGRAM

### COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF AUGUST 2024

#### Precinct 3

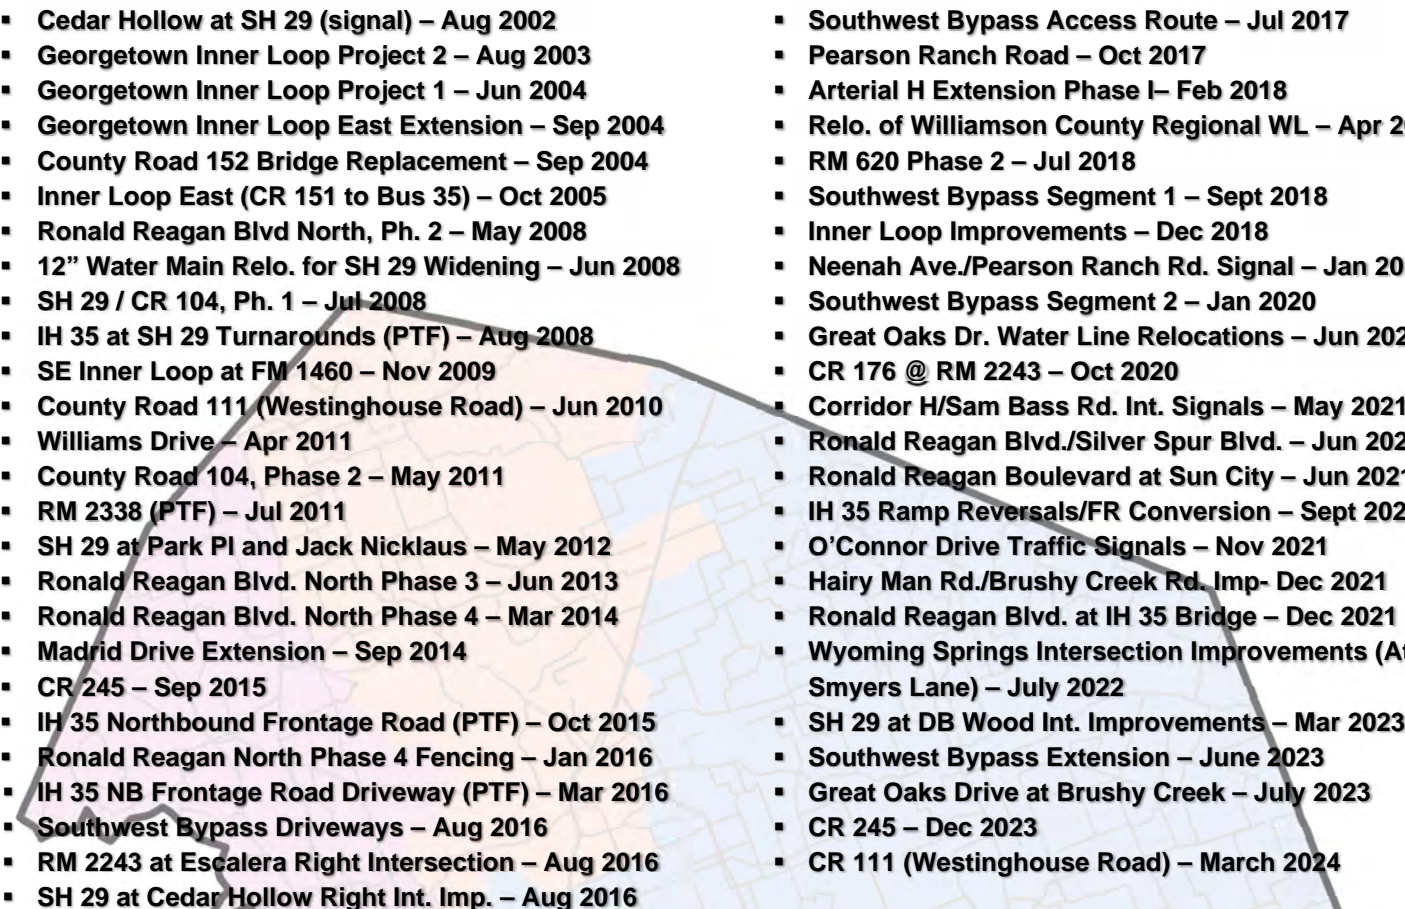- 
- Cedar Hollow at SH 29 (signal) – Aug 2002
  - Georgetown Inner Loop Project 2 – Aug 2003
  - Georgetown Inner Loop Project 1 – Jun 2004
  - Georgetown Inner Loop East Extension – Sep 2004
  - County Road 152 Bridge Replacement – Sep 2004
  - Inner Loop East (CR 151 to Bus 35) – Oct 2005
  - Ronald Reagan Blvd North, Ph. 2 – May 2008
  - 12” Water Main Relo. for SH 29 Widening – Jun 2008
  - SH 29 / CR 104, Ph. 1 – Jul 2008
  - IH 35 at SH 29 Turnarounds (PTF) – Aug 2008
  - SE Inner Loop at FM 1460 – Nov 2009
  - County Road 111 (Westinghouse Road) – Jun 2010
  - Williams Drive – Apr 2011
  - County Road 104, Phase 2 – May 2011
  - RM 2338 (PTF) – Jul 2011
  - SH 29 at Park Pl and Jack Nicklaus – May 2012
  - Ronald Reagan Blvd. North Phase 3 – Jun 2013
  - Ronald Reagan Blvd. North Phase 4 – Mar 2014
  - Madrid Drive Extension – Sep 2014
  - CR 245 – Sep 2015
  - IH 35 Northbound Frontage Road (PTF) – Oct 2015
  - Ronald Reagan North Phase 4 Fencing – Jan 2016
  - IH 35 NB Frontage Road Driveway (PTF) – Mar 2016
  - Southwest Bypass Driveways – Aug 2016
  - RM 2243 at Escalera Right Intersection – Aug 2016
  - SH 29 at Cedar Hollow Right Int. Imp. – Aug 2016
  - Southwest Bypass Access Route – Jul 2017
  - Pearson Ranch Road – Oct 2017
  - Arterial H Extension Phase I – Feb 2018
  - Relo. of Williamson County Regional WL – Apr 2018
  - RM 620 Phase 2 – Jul 2018
  - Southwest Bypass Segment 1 – Sept 2018
  - Inner Loop Improvements – Dec 2018
  - Neenah Ave./Pearson Ranch Rd. Signal – Jan 2019
  - Southwest Bypass Segment 2 – Jan 2020
  - Great Oaks Dr. Water Line Relocations – Jun 2020
  - CR 176 @ RM 2243 – Oct 2020
  - Corridor H/Sam Bass Rd. Int. Signals – May 2021
  - Ronald Reagan Blvd./Silver Spur Blvd. – Jun 2021
  - Ronald Reagan Boulevard at Sun City – Jun 2021
  - IH 35 Ramp Reversals/FR Conversion – Sept 2021
  - O’Connor Drive Traffic Signals – Nov 2021
  - Hairy Man Rd./Brushy Creek Rd. Imp- Dec 2021
  - Ronald Reagan Blvd. at IH 35 Bridge – Dec 2021
  - Wyoming Springs Intersection Improvements (At Smyers Lane) – July 2022
  - SH 29 at DB Wood Int. Improvements – Mar 2023
  - Southwest Bypass Extension – June 2023
  - Great Oaks Drive at Brushy Creek – July 2023
  - CR 245 – Dec 2023
  - CR 111 (Westinghouse Road) – March 2024

# WILLIAMSON COUNTY

## ROAD BOND PROGRAM


### COMPLETED PROJECTS

CONSTRUCTION SUBSTANTIALLY COMPLETE/OPEN TO TRAFFIC - AS OF AUGUST 2024

#### Precinct 4


- Bridge RPLs (CR 390, 406 & 427) – Nov 2002
- County Road 368 and 369 – Nov 2002
- County Road 412 – Aug 2003
- County Road 300 and 301 – Dec 2003
- County Road 424 Bridge RPL – Jan 2004
- Chandler Rd. Extension, Ph. 1 – Mar 2005
- County Road 112, Ph. 1 – Aug 2005
- County Road 137 – Oct 2005
- Limmer Loop, Ph. 1A – Jul 2006
- Chandler Rd, Ph. 2 – Dec 2007
- Limmer Loop, Ph. 1B – Mar 2008
- Limmer Loop, Ph. 1C – Oct 2008
- US 79, Section 5B (PTF) – Aug 2010
- Chandler Rd, Ph. 3B – Oct 2010
- US 79, Section 5A (PTF) – May 2011
- FM1660 at Landfill Rd. – Sep 2011
- Second Street Drainage Imp. – Dec 2011
- US 79 Section 3 (PTF) – Jul 2012
- Chandler Rd, Ph. 3A – Dec 2012
- Second Street Roadway Imp. – Feb 2013
- County Road 138 – Jun 2013
- County Road 108 – Nov 2013
- County Road 170 – Feb 2015
- Multi-Site Traffic Signals – Jun 2016
- Bill Pickett Trail– Nov 2016
- County Road 110 South – May 2018
- County Road 119 – Mar 2019
- County Road 110 Middle – Oct 2020
- CR Paving (401, 402 & 404) – Nov 2021
- Thrall Project (S. Bounds Street) – Jan 2022
- Bartlett Project (Cotrell Street) – Feb 2022
- County Road 101 – Feb 2022
- Davilla Street Culvert Re – June 2022
- Coupland Project – June 2022
- CR 404 Hutto Water Line – Sept 2022
- University Boulevard Widening – Apr 2023
- University Boulevard (Chandler Road) Expansion – May 2023
- CR 401 Reconstruction – July 2023
- CR 404 and FM 973 Improvements – July 2023
- Bud Stockton Extension – Aug 2023
- East Wilco Hwy (SE Loop Seg 1) – Aug 2023
- Samsung Hwy (Future County Rd) – Aug 2023
- Samsung Hwy (CR 404 Realign.) – Oct 2023
- CR 307 Reconstruction – Feb 2024
- CR 138 Right Turn Lane at SH 130 – May 2024
- CR 332 Realignment – July 2024
- CR 366 – August 2024

## 2000/2006 Road Bond Program Projects Precinct 1 - Commissioner Cook

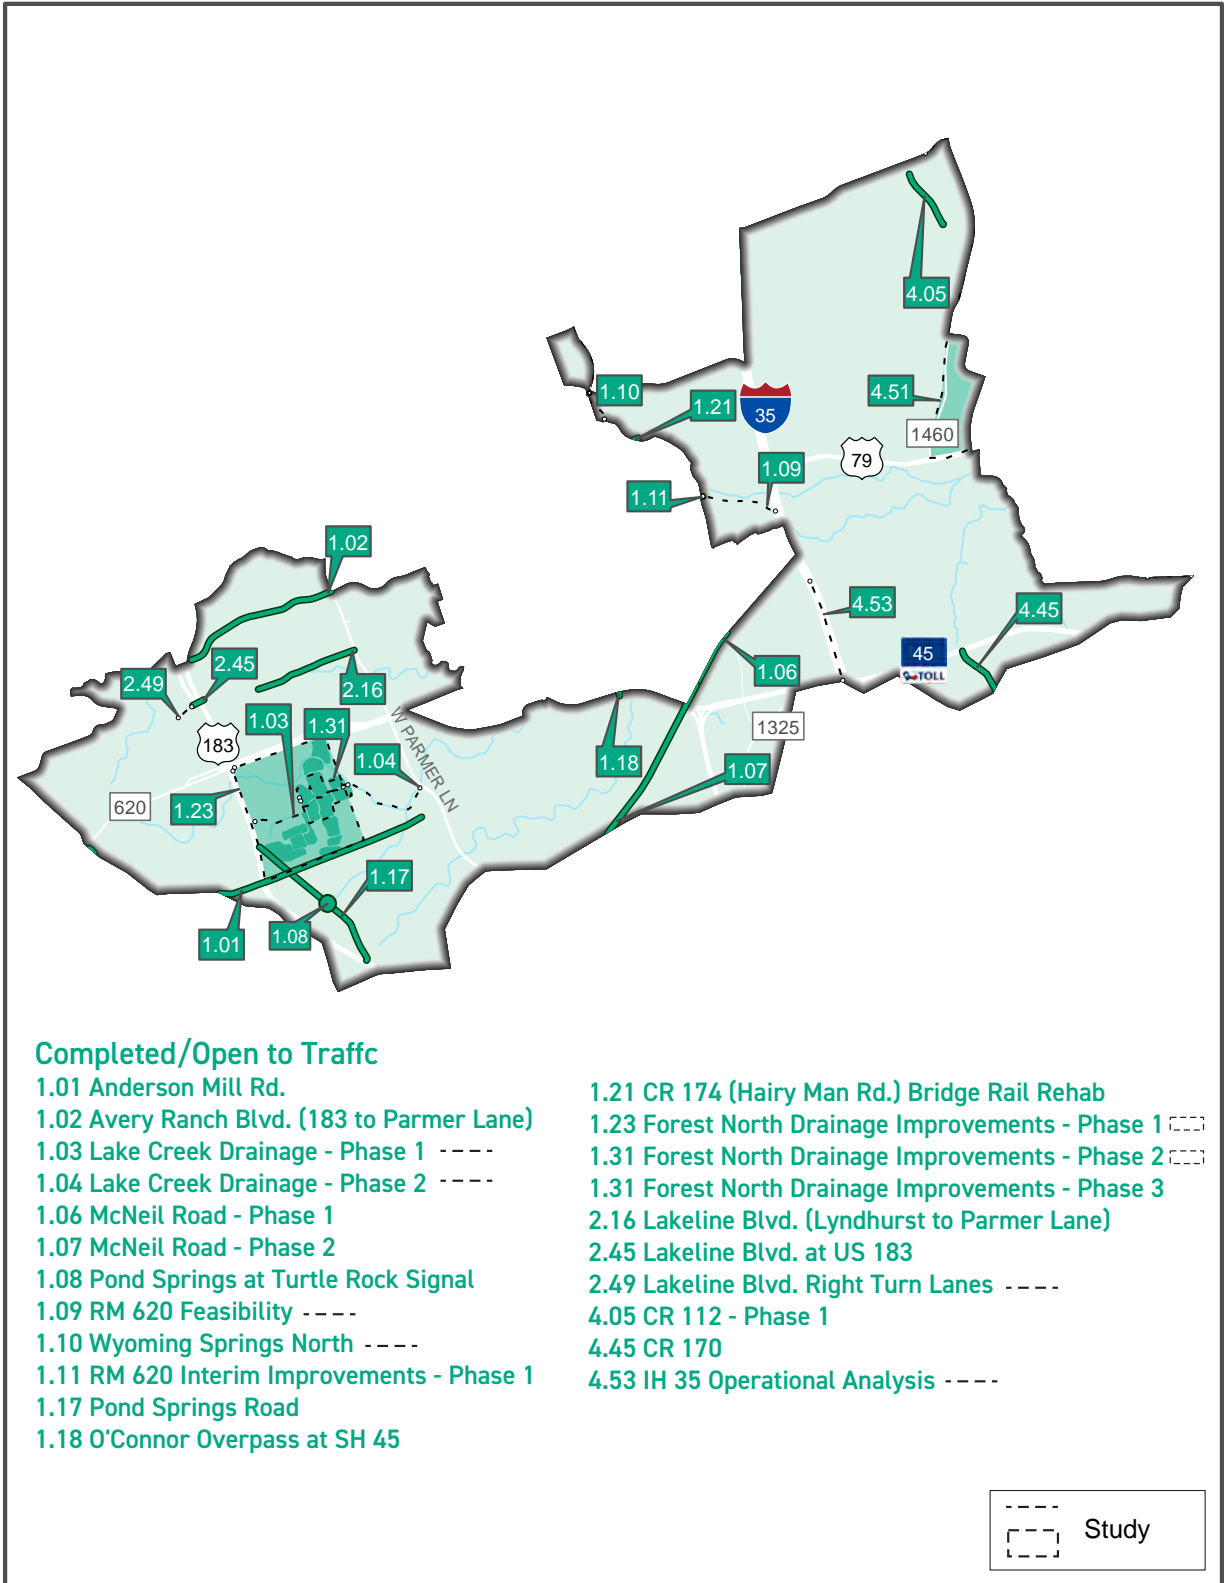

# 2013 ROAD BOND PROGRAM PROJECTS


## Precinct 1 - Commissioner Cook

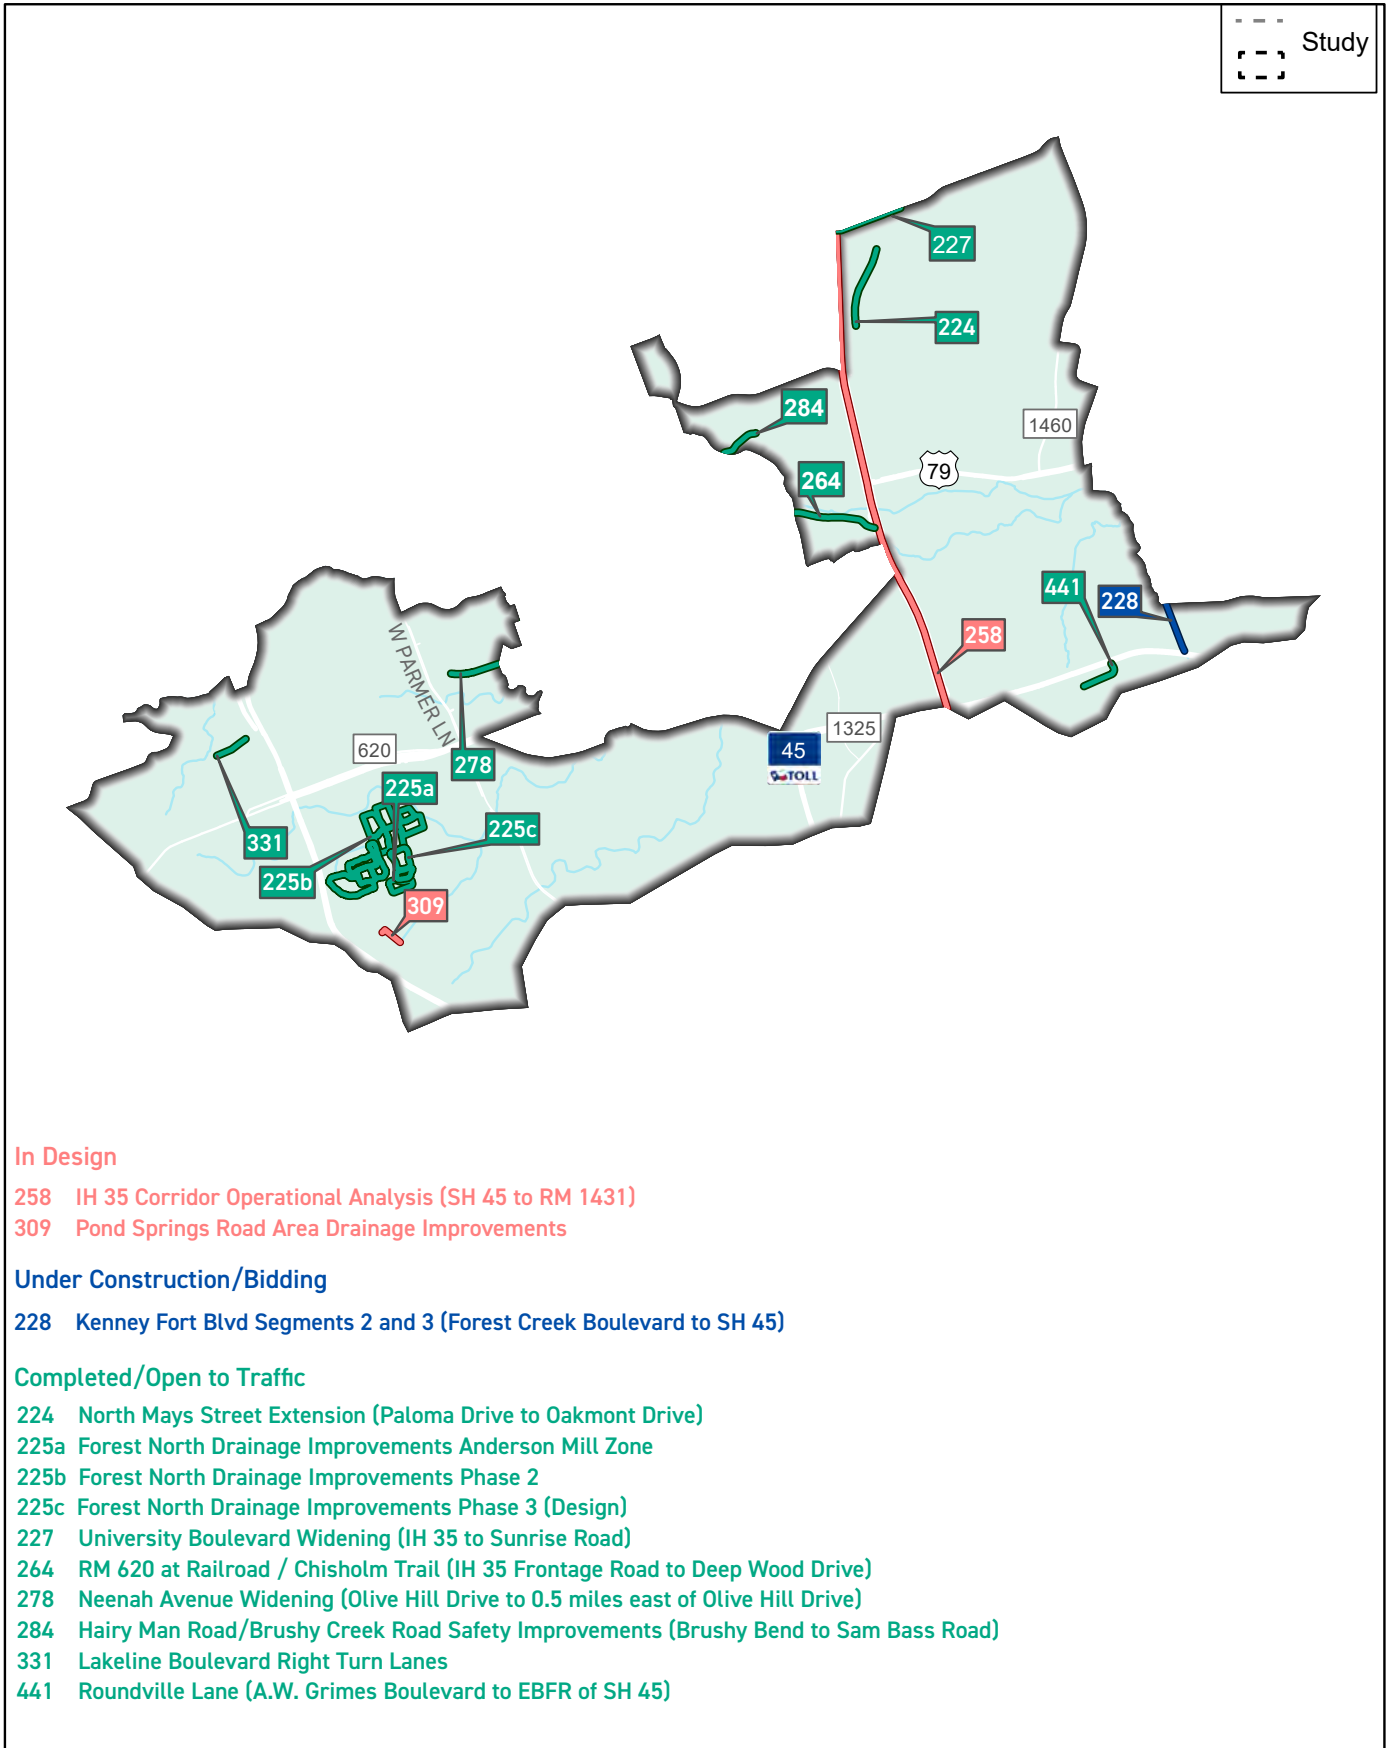




# 2019 ROAD BOND PROGRAM PROJECTS

## Precinct 1 - Commissioner Cook

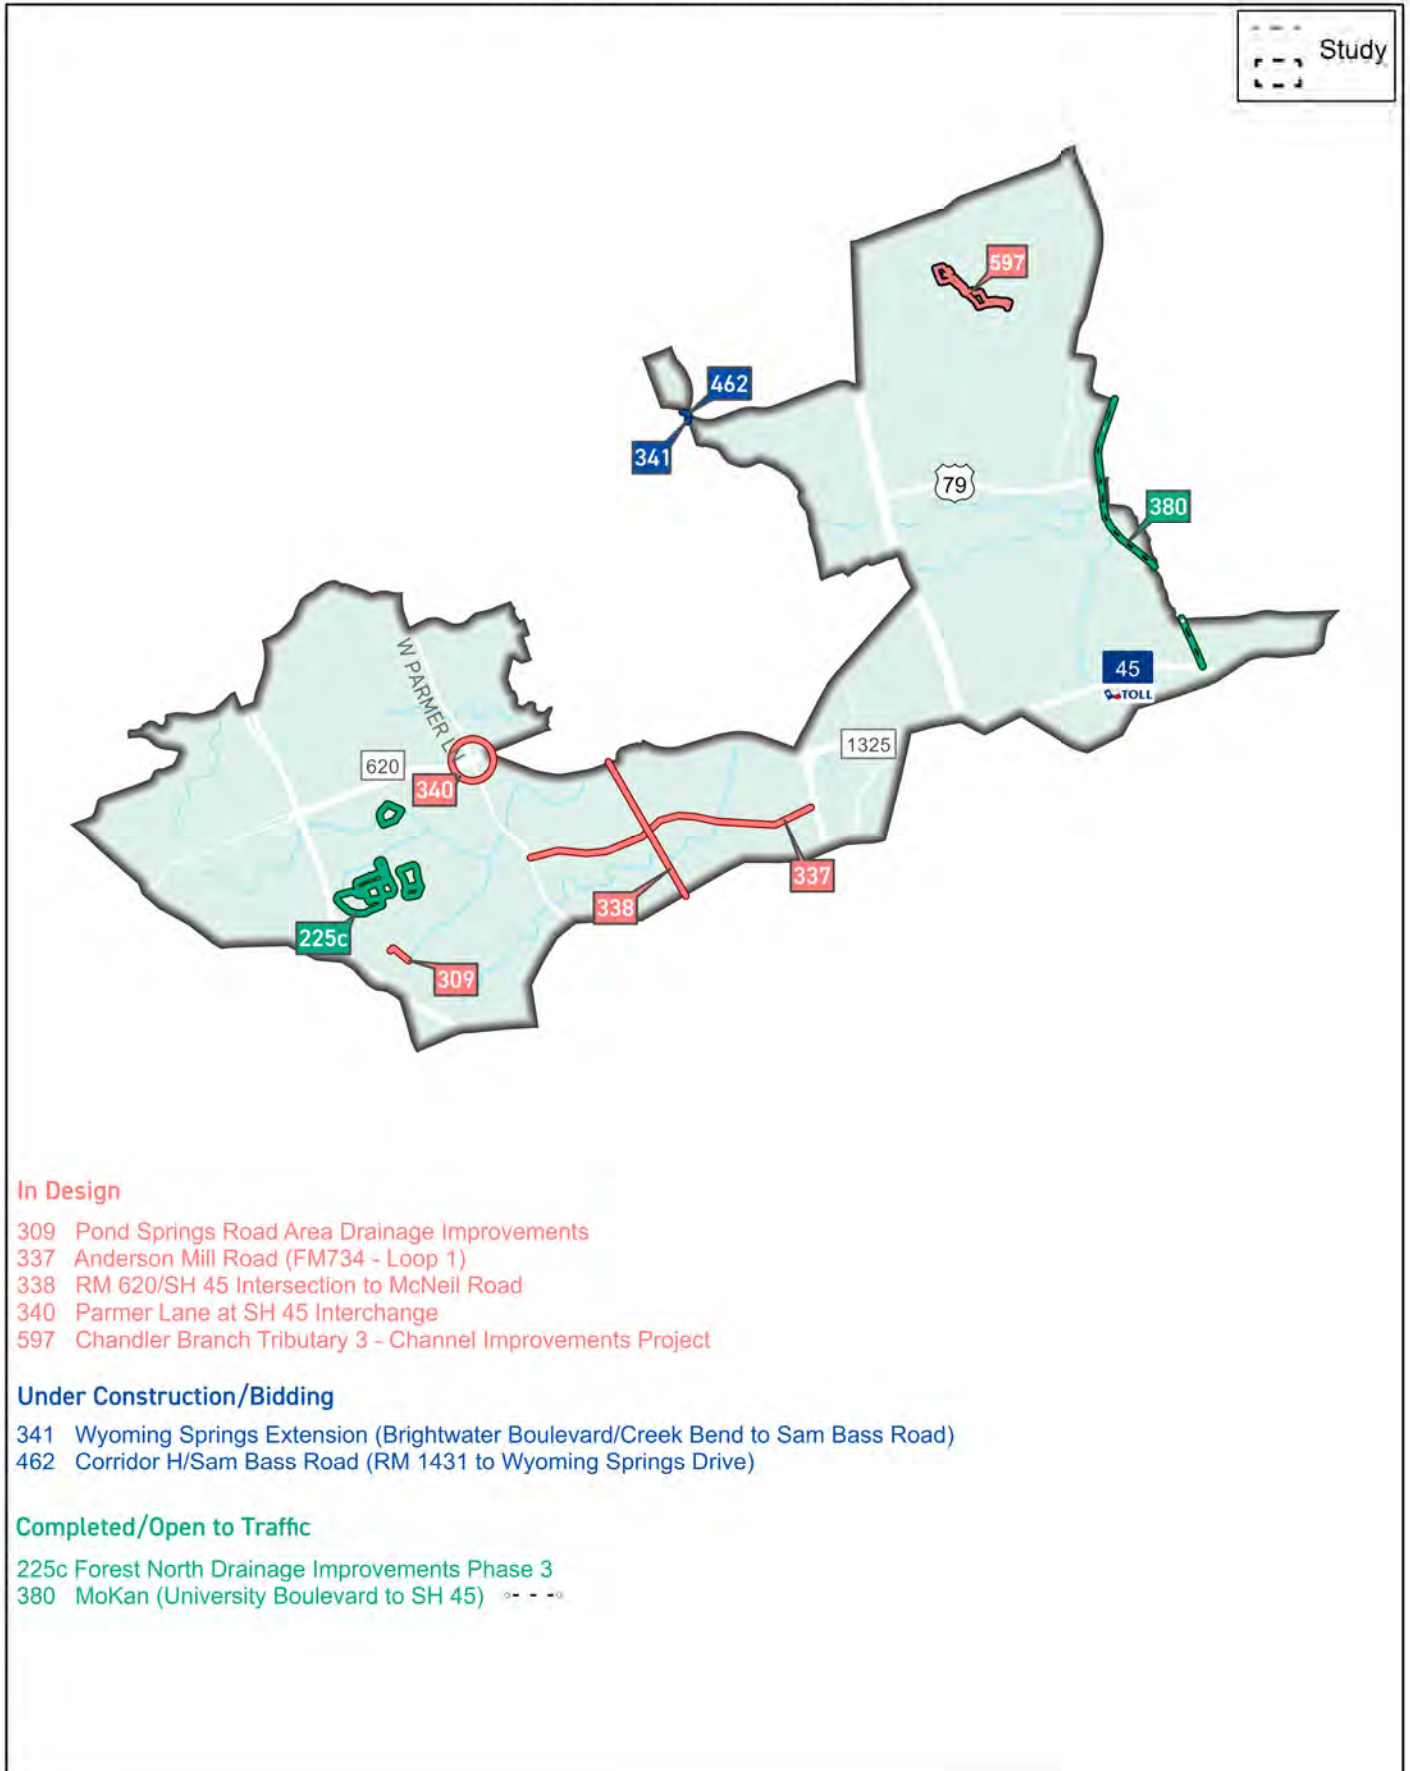

# 2023 ROAD BOND PROGRAM PROJECTS



## Precinct 1 - Commissioner Cook

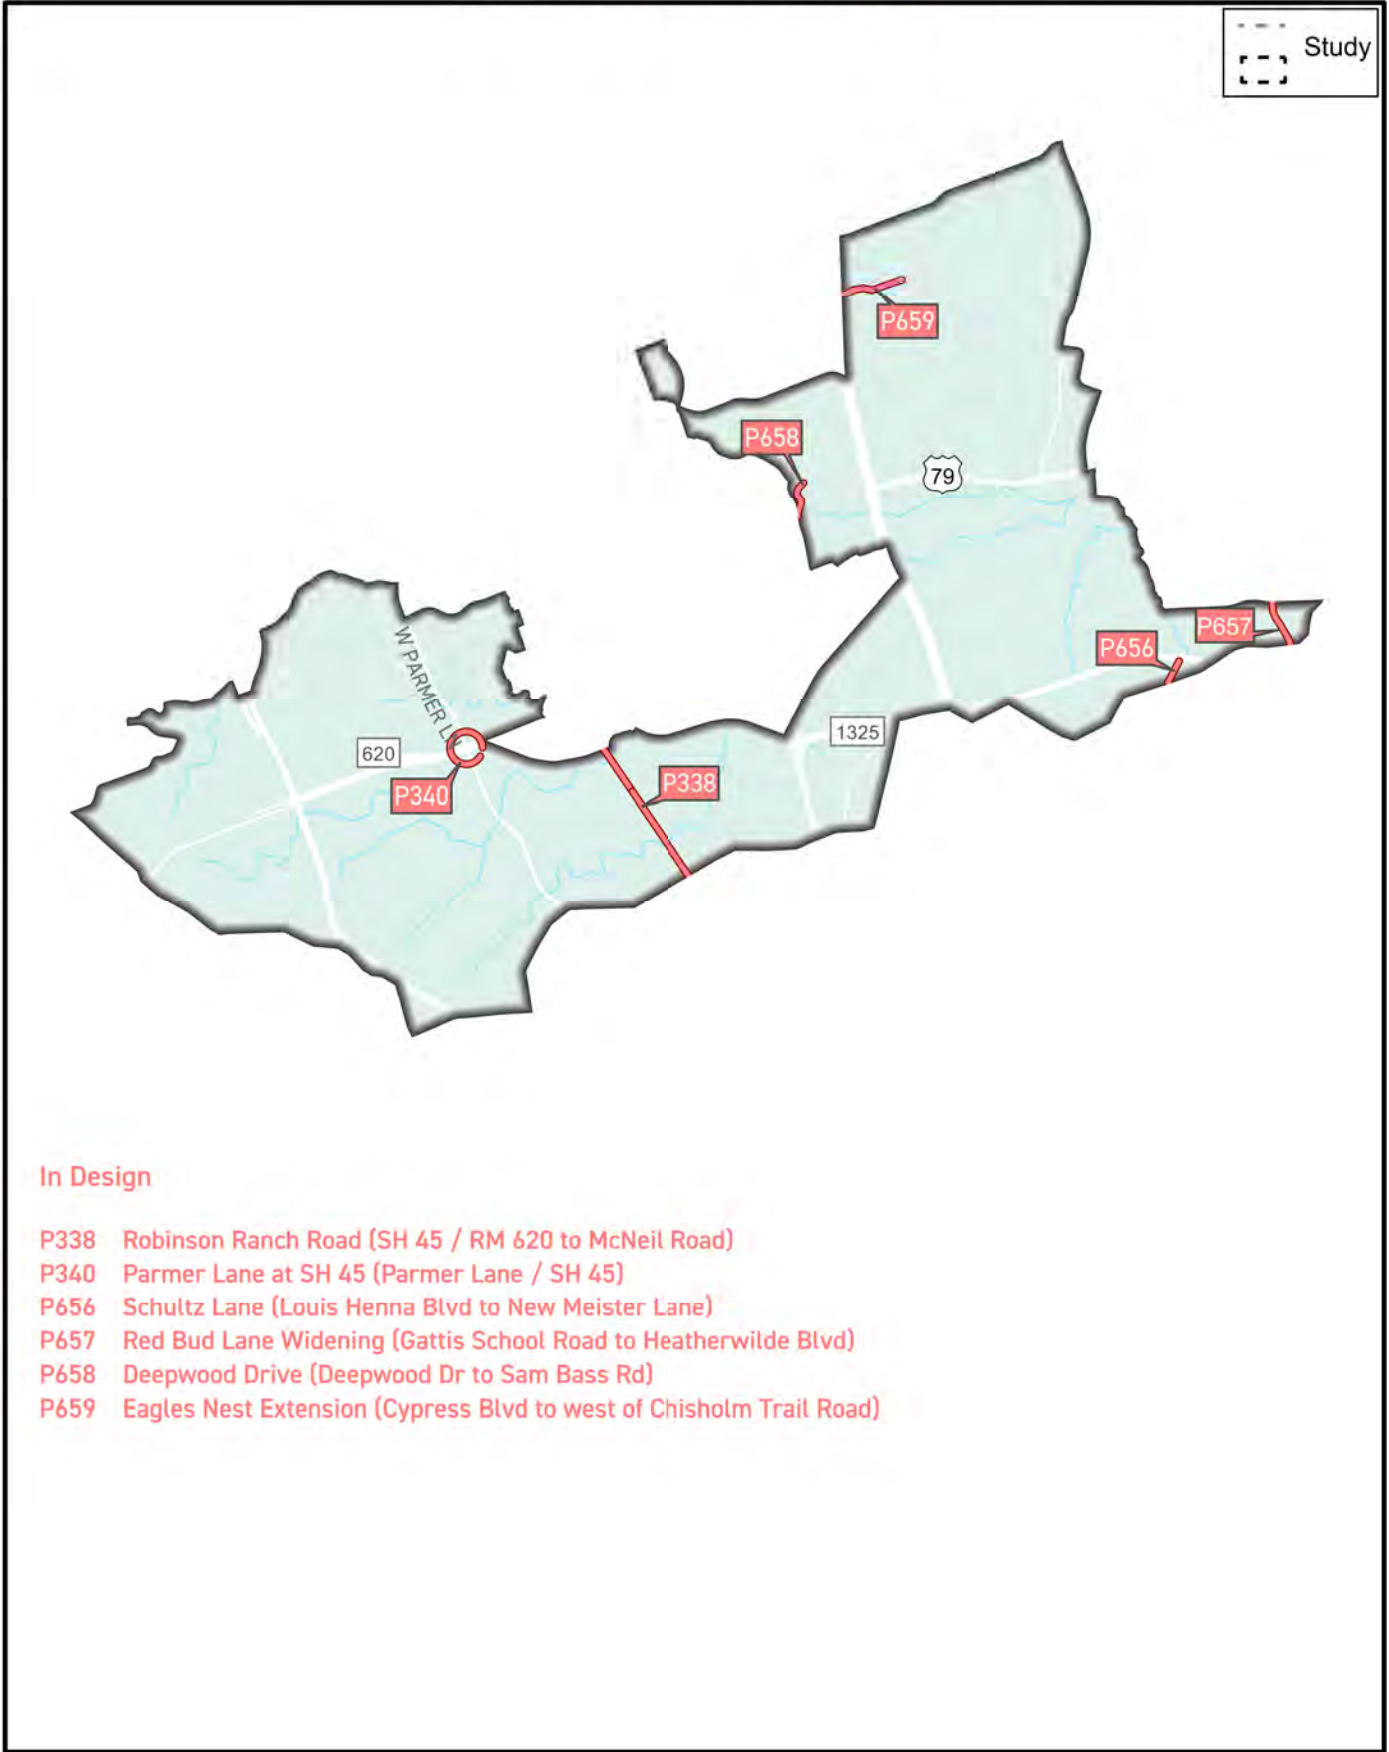



# 2013 ROAD BOND PROGRAM PROJECTS

## Precinct 2 - Commissioner Long

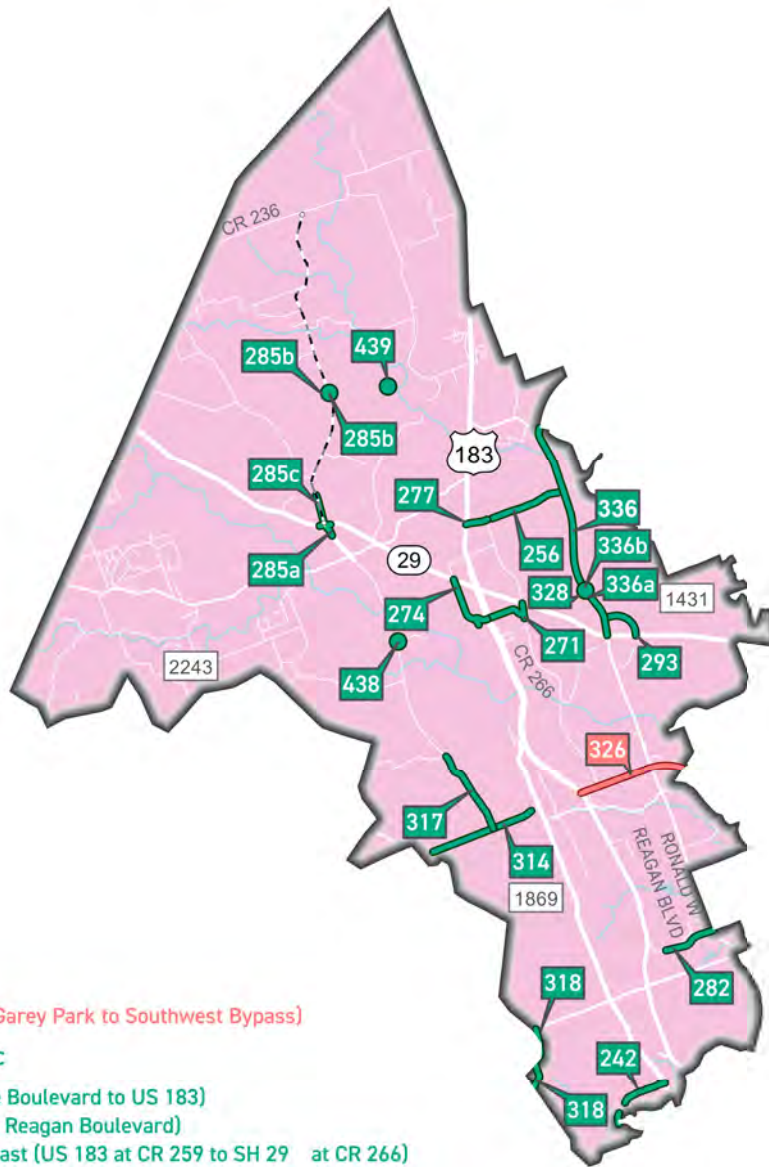

### In Design

326 RM 2243 Realignment (Garey Park to Southwest Bypass)



### Completed/Open to Traffic

- 242 Little Elm Trail (Lakeline Boulevard to US 183)
- 256 CR 258 (Sunset Ridge to Reagan Boulevard)
- 271 Seward Junction Southeast (US 183 at CR 259 to SH 29 at CR 266)
- 274 Seward Junction Southwest (SH 29 at CR 213 to US 183 at CR 259)
- 277 CR 258 Extension (US 183 to Sunset Ridge Drive)
- 282 New Hope Drive Phase 1 (Cottonwood Creek Trail to Ronald Reagan Boulevard)
- 285 CR 200 Study and Schematic (SH 29 to CR 236)
- 285a State Highway 29 Intersection at CR 200/Loop 332
- 285b CR 200 at Bold Sundown Left Turn Lane
- 285c CR 200 (CMTA Railroad to CR 201)
- 293 Kauffman Loop Phase 1 - Two Lanes (northeast quadrant of Reagan at SH 29)
- 314 Old 2243/Hero Way West (Lakeline Boulevard to west of US 183)
- 317 Bagdad Road North (Collaborative Way to RM 2243)
- 318 Anderson Mill Road (Gaspar Bend to RM 1431)
- 328 Ronald Reagan at Santa Rita
- 336 Ronald Reagan Boulevard Widening (SH 29 to FM 3405) - - - -
- 336a Ronald Reagan Boulevard Widening & Temp Signals at Santa Rita Boulevard
- 336b Ronald Reagan Safety Improvements
- 438 Bagdad Road (CR 279) at CR 278 (River Ranch County Park Road)
- 439 San Gabriel Ranch Road Bridge at Lackey Creek



# 2019 ROAD BOND PROGRAM PROJECTS

## Precinct 2 - Commissioner Long

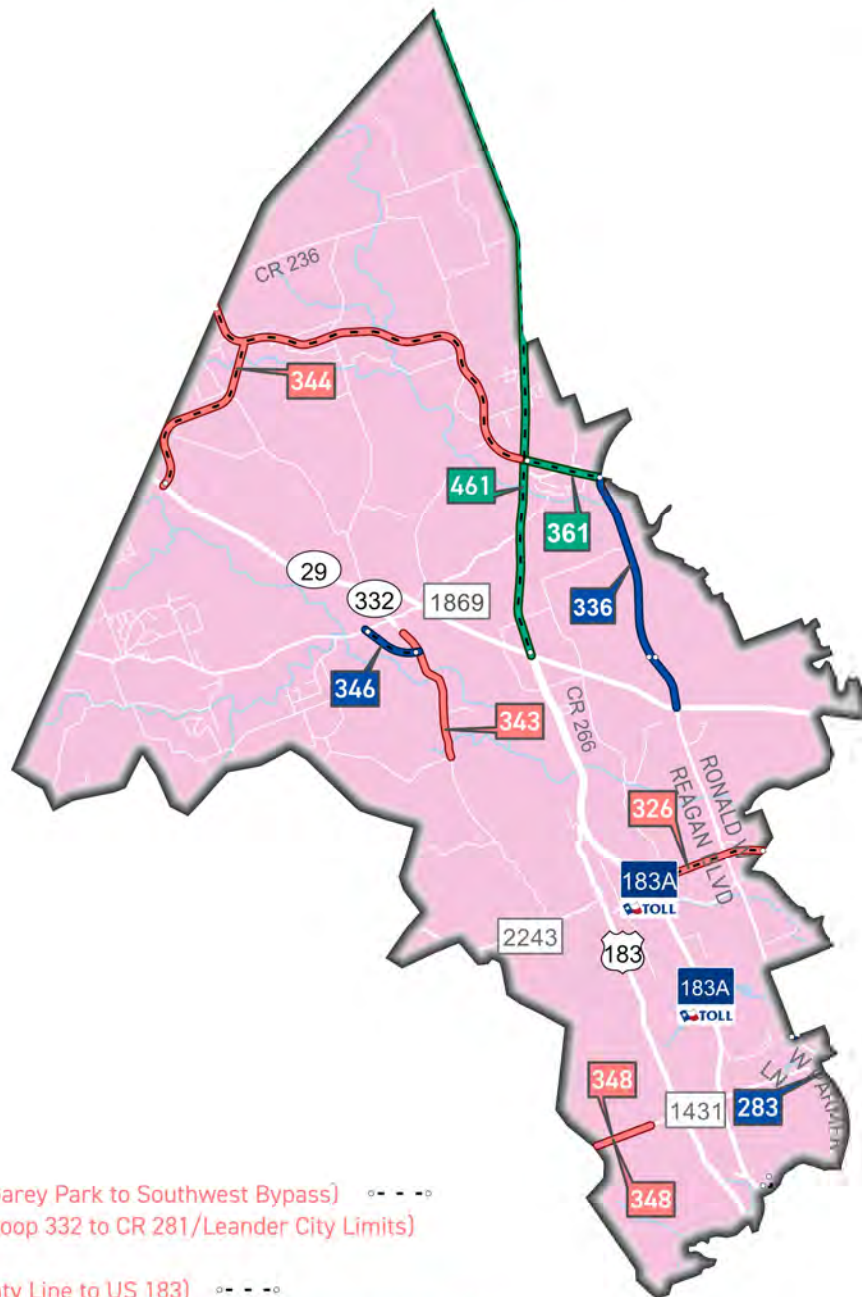

### In Design

- 326 RM 2243 Realignment (Garey Park to Southwest Bypass) - - - -
- 343 Bagdad Road /CR 279 (Loop 332 to CR 281/Leander City Limits) to Sam Bass Road
- 344 Corridor I2 (Burnet County Line to US 183) - - - -
- 348 Whitestone Boulevard Widening (Bagdad Road to Anderson Mill Road)

### Under Construction/Bidding

- 283 New Hope Drive Extension Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)
- 336 Ronald Reagan Boulevard Widening (SH 29 to FM 3405)
- 346 Liberty Hill (SH 29) Bypass (RM 1869 to CR 279)


### Completed/Open to Traffic

- 361 Corridor I1 (FM 3405) (Ronald Reagan Boulevard to US 183)
- 461 Corridor F/US 183 (Williamson/Burnet County Line to SH 29) - - - -

# 2023 ROAD BOND PROGRAM PROJECTS

## Precinct 2 - Commissioner Long

Study

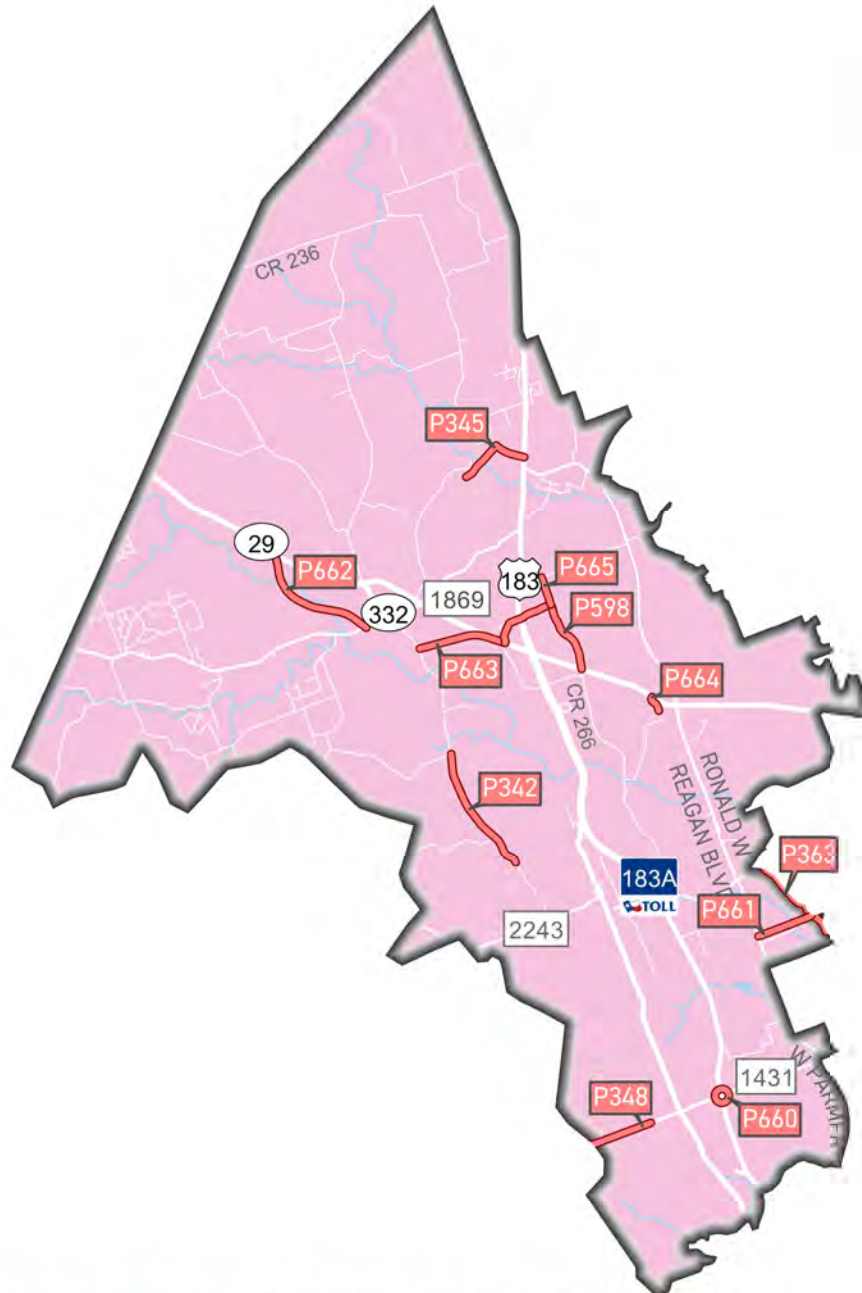

### In Design

- P342 Bagdad Road (North of San Gabriel Parkway to CR 281 / Leander City Limits)
- P345 CR 214 (End of CR 214 to US 183)
- P348 Whitestone Boulevard Widening (west of Anderson Mill to Bagdad Road)
- P363 CR 175 (South of Creek Meadow Cove to RM 2243)
- P598 Seward Junction Loop (SH 29/CR 260 to SH 29/CR 213)
- P660 RM 1431 at 183A Intersection
- P661 Crystal Falls Parkway (Ronald Reagan Blvd to CR 175)
- P662 Liberty Hill Bypass West (SH 29 (west of Liberty Hill High School) to RM 1869)
- P663 Liberty Hill Bypass East (Bagdad Road/CR 279 to SH 29)
- P664 Kauffman Loop (SH 29 to north terminus of Kauffman Loop)
- P665 CR 258 (Seward Junction Loop to CR 258 Extension)

**Project Name: CR 258 Extension**  
**Project No. 22IFB141**

Original Contract Price = \$5,836,754.36

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
9/14/2022	9/27/2022	11/28/2022	12/8/2022	12/14/2023		395	-29	366

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	11/1/2022	11/30/2022	0	\$47,590.20	\$47,590.20	\$5,287.80	\$5,287.80	1	0
2	12/1/2022	1/31/2023	55	\$536,565.20	\$584,155.40	\$59,618.36	\$64,906.16	10	15
3	2/1/2023	2/28/2023	28	\$463,314.38	\$1,047,469.78	\$51,479.37	\$116,385.53	17	23
4	3/1/2023	3/31/2023	31	\$354,614.85	\$1,402,084.63	\$39,401.65	\$155,787.18	23	31
5	4/1/2023	4/30/2023	30	\$455,839.20	\$1,857,923.83	\$50,648.80	\$206,435.98	31	39
6	5/1/2023	5/31/2023	31	\$1,166,374.04	\$3,024,297.87	\$129,597.12	\$336,033.10	50	48
7	6/1/2023	6/30/2023	30	\$1,003,480.88	\$4,027,778.75	-\$124,044.74	\$211,988.36	64	56
8	7/1/2023	7/31/2023	31	\$614,801.35	\$4,642,580.10	\$32,357.96	\$244,346.32	73	64
9	8/1/2023	8/31/2023	31	\$170,332.60	\$4,812,912.70	\$8,964.87	\$253,311.19	76	73
10	9/1/2023	9/30/2023	30	\$192,986.82	\$5,005,899.52	\$10,157.21	\$263,468.40	79	81
11	10/1/2023	10/31/2023	31	\$175,527.78	\$5,181,427.30	\$9,238.30	\$272,706.70	82	90
12	11/1/2023	11/30/2023	30	\$235,724.29	\$5,417,151.59	\$12,406.54	\$285,113.24	86	98
13	12/1/2023	12/31/2023	14	\$252,218.57	\$5,669,370.16	\$13,274.66	\$298,387.90	89	102
14	1/1/2024	1/31/2024	0	\$268,770.72	\$5,938,140.88	-\$177,201.35	\$121,186.55	91	102
15	2/1/2024	7/31/2024	0	\$66,141.40	\$6,004,282.28	\$1,349.82	\$122,536.37	92	102

8/31/2024 Comments- Project close out in progress.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	11/11/2022	\$ -	\$ -

4B: Third Party Accommodation. Third party requested work. This Change Order modifies the Contract to require that City of Georgetown, (collectively referred to as the "City") be an additional insured to Joe Bland Construction's, L.P. (Contractor) commercial general liability (CGL) insurance policy and to their commercial auto liability (Auto Liability) insurance policy. Adding the City to the Contractor's insurance was in the terms and conditions of the Interlocal Agreement between the City and Williamson County.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	11/22/2022	\$ 422,565.69	\$ 422,565.69

3. County Convenience 3F: Additional Work Desired By The County: This Change Order adds items to the Contract for safety improvements needed at Ronald Reagan and Elizabeth Parkway. Ronald Reagan will be widened along the west side of the roadway to allow for a left turn lane into Elizabeth Parkway.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	6/6/2023	22,263.50	444,829.19

4D. Third Party Accommodation. Other. This Change Order compensates the Contractor for additional work to install sleeves for future utilities across CR 258 and Questa Trail. The payment will be split between the Developer and Williamson County. This method of payment was agreed on between the Developer and Williamson County.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	8/1/2023	-153,292.00	291,537.19


5A. Contractor exercises option to change the traffic control plan. This Change Order removes the unnecessary traffic control and construction items from the Contract, per the agreement to completely close existing CR 258 for the duration of Summer. This Change Order also revises the Disincentive dollar amount in the Project Construction Manual to \$1,250/day. 1B. Design Error or Omission. This Change Order also revises the Unit of Measure for the asphalt items that were added in Change Order #2.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	9/14/2023	539,623.96	831,161.15

4B. Third Party Accommodation. Third party requested work. This Change Order provides payment to the contractor for widening the eastbound pavement, adding a right turn lane/driveway into Liberty Hill's proposed High School, and relocating an existing water line out from under the new Liberty Hill High School driveway. LHISD will reimburse the County 100%.

Adjusted Price = \$6,667,915.51



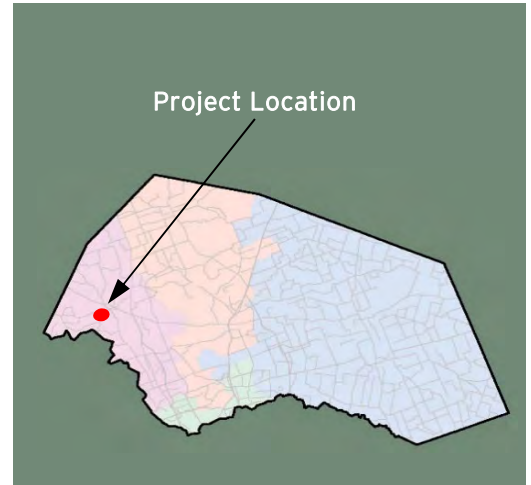

**Liberty Hill Bypass Improvements  
(RM 1869 to CR 279)**

**Project Length: 2.316 Miles**  
**Roadway Classification: Bagdad Road (Arterial);  
 Liberty Hill Bypass (Minor Arterial)**

**Project Schedule: February 2024 - Late 2025**  
**Estimated Construction Cost: \$14.2 Million**



**AUGUST 2024 IN REVIEW**

8/2/24: Chasco Constructors completed the paving along FM 1869 and continued processing flexible base along Liberty Hill Bypass. Subcontractor DIJ restriped FM 1869 for the new traffic pattern.

8/9/24: Chasco finished forming and poured the upstream headwall at the culvert on FM 1869 and continued forming concrete riprap at various locations throughout the project.

8/16/24: Chasco Constructors continued processing flexible base from the Tributary 1 Bridge to the east and spreading topsoil at various locations on the project.

8/23/24: Chasco continued forming concrete riprap at various locations throughout the project.

8/30/24: Chasco began clearing the right-of-way on the north end of Bagdad Road. Subcontractor Lone Star Paving placed prime between Tributary 1 bridge and Tributary 2 bridge.



Design Engineer: LJA  
 Contractor: Chasco Constructors  
 Construction Observation:  
 Bruce Thurin, HNTB

Williamson County  
 Road Bond Program





**Liberty Hill Bypass (SH 29) Bypass  
Project No. 24IFB15**

Original Contract Price = \$14,149,449.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/5/2023	12/12/2023	2/5/2024	2/15/2024			652		652	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>
1	2/5/2024	2/29/2024	15	\$1,167,168.15	\$1,167,168.15	\$129,685.35	\$129,685.35	9	2
2	3/1/2024	3/31/2024	31	\$1,206,856.44	\$2,374,024.59	\$134,095.16	\$263,780.51	18	7
3	4/1/2024	4/30/2024	30	\$1,527,575.22	\$3,901,599.81	\$169,730.58	\$433,511.09	30	12
4	5/1/2024	5/31/2024	31	\$681,539.40	\$4,583,139.21	\$75,726.60	\$509,237.69	35	16
5	6/1/2024	6/30/2024	30	\$661,450.37	\$5,244,589.58	\$73,494.49	\$582,732.18	40	21
6	7/1/2024	7/31/2024	31	\$456,995.73	\$5,701,585.31	\$50,777.30	\$633,509.48	44	26

8/31/2024      Comments -      The contractor continued processing flexible base from the Tributary 1 Bridge to the east and spreading topsoil at various locations throughout the project. The contractor placed prime between Tributary 1 bridge and Tributary 2 bridge. The contractor began placing seed and fertilizer along the south side of FM 1869 and along Liberty Hill Bypass from FM 1869 to the entrance of the Williamson County Probation Office.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	4/17/2024	\$ 29,260.00	\$ 29,260.00

2. Differing Site Conditions (unforeseeable) 2G: Unadjusted utility (unforeseeable): This Change Order compensates the Contractor for lowering and encasing existing water service lines to the Williamson County Adult Probation Center and Parcel 41. The service lines will be lowered and encased 2 and ½ feet below finish grade of the ditches. This will allow for water service to be maintained across the proposed roadway, allows the lines to be removed if needed for any repairs and will not compromise the roadway structure if they do need future repairs.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	6/24/2024	\$ 21,500.00	\$ 50,760.00

6D. Untimely ROW/Utilities. Right-of-Way not clear (County responsibility for ROW). This Change Order compensates the Contractor for clearing the PEC easement to expedite the relocation process.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	7/3/2024	\$ 229,702.00	\$ 280,462.00

3M. County Convenience. Other.: The City of Liberty Hill's water line project was delayed until the first quarter of 2025, Originally , this was scheduled to be clear in October of 2024. It has been decided to add the water line work to the LHB roadway project via Change Order to Williamson County's project. this will help avoid delays of the roadway construction.

Adjusted Price = \$14,429,911.00

**Ronald Reagan Boulevard Widening  
Project No. 24IFB57**

Original Contract Price = \$52,159,299.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
6/25/2024	7/16/2024	8/22/2024	9/3/2024			1035		1035


8/31/2024      Comments - Notice of Award was granted on 8/22/24 and work will commence on 9/3/24. The Contractor excavated and began installing ductile iron pipe for the City of Georgetown water line from Kaufman Loop to Santa Rita Boulevard. The Contractor began clearing the right-of-way and excavating between the Tributary 1 Bridge and Sowe's Branch Bridge.

Adjusted Price = \$52,159,299.00



# 2013 ROAD BOND PROGRAM PROJECTS



## Precinct 3 - Commissioner Covey

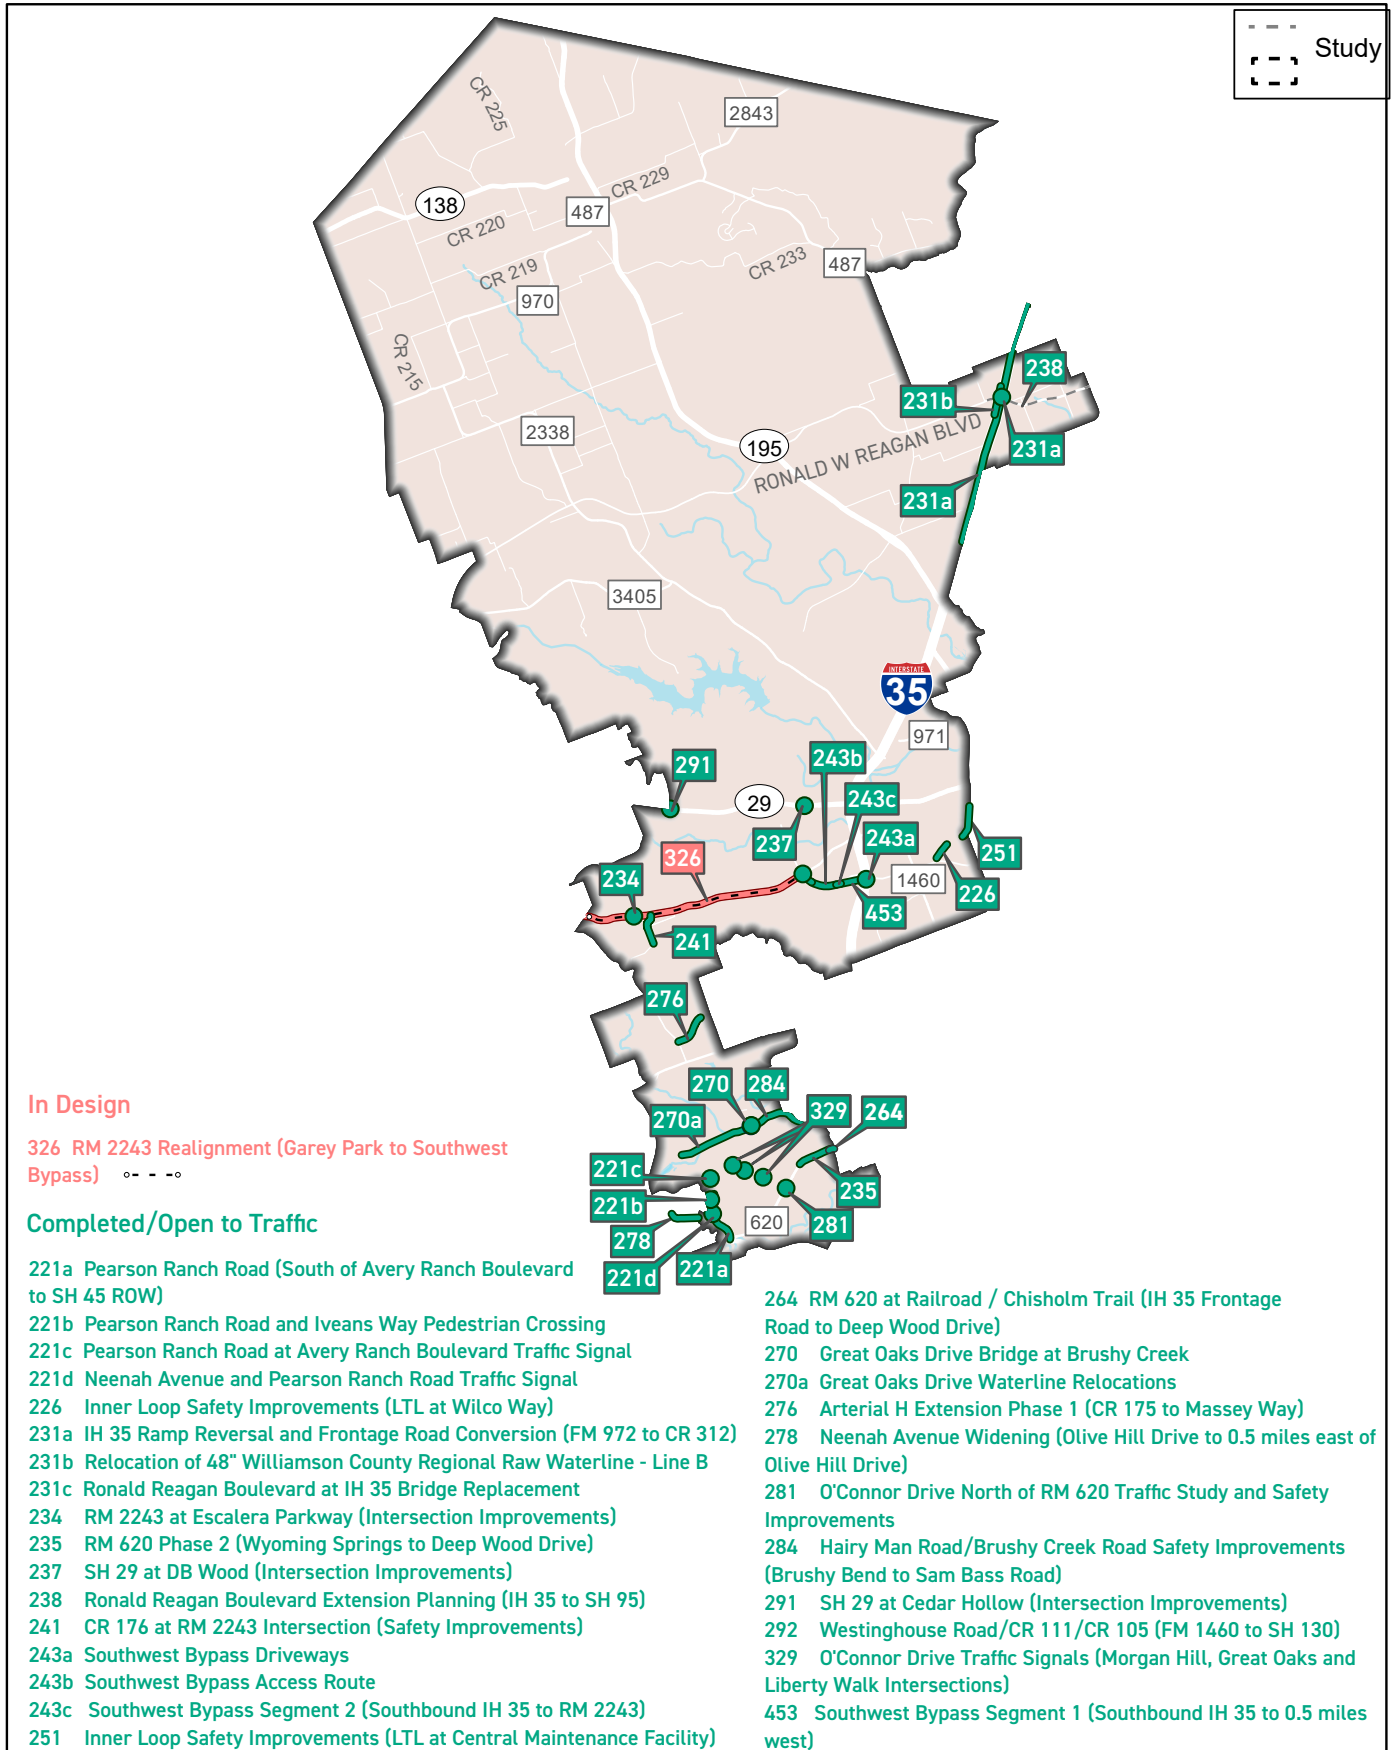



# 2019 ROAD BOND PROGRAM PROJECTS

## Precinct 3 - Commissioner Covey

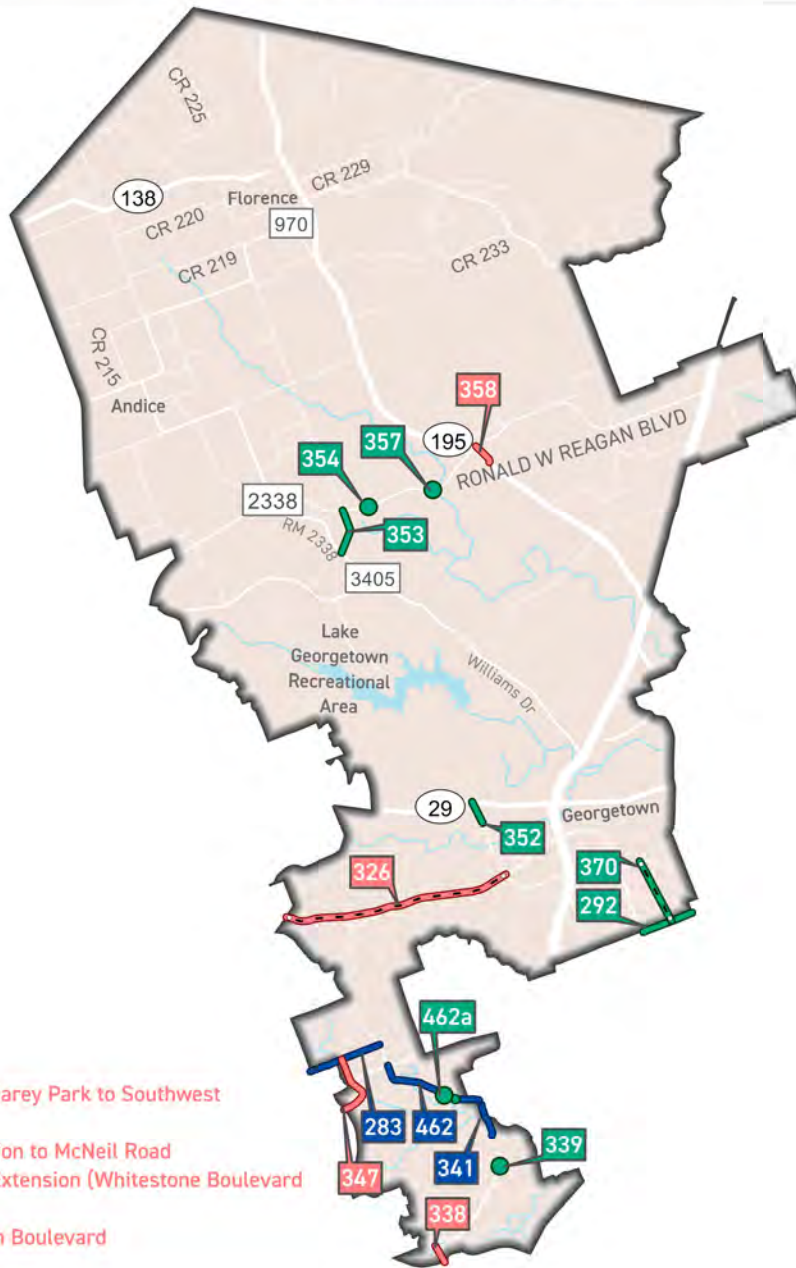

### In Design

- 326 RM 2243 Realignment (Garey Park to Southwest Bypass) - - - -
- 338 RM 620/SH 45 Intersection to McNeil Road
- 347 Toro Grande Boulevard Extension (Whitestone Boulevard to Parmer Lane)
- 358 SH 195 at Ronald Reagan Boulevard

### Under Construction/Bidding


- 283 New Hope Drive Extension Phase 2A (Ronald Reagan Boulevard to Sam Bass Road)
- 341 Wyoming Springs Extension (Brightwater Boulevard/ Creek Bend to Sam Bass Road)
- 462 Corridor H/Sam Bass Road (RM 1431 to Wyoming Springs Drive)

### Completed/Open to Traffic

- 292 CR 111/CR 105 Westinghouse (FM 1460 to SH 130)
- 339 Wyoming Springs Improvements (At Smyers Lane)
- 352 Southwest Bypass Extension (SH 29 to Wolf Ranch Parkway)
- 353 CR 245 (North of RM 2338 to Ronald Reagan Boulevard)
- 354 Ronald Reagan at Silver Spur Boulevard
- 357 Ronald Reagan at Sun City Boulevard
- 370 MoKan (Georgetown Inner Loop to University Boulevard) - - - -
- 462a Corridor H/Sam Bass Road Interim Traffic Signals (Walsh Ranch and Great Oaks Drive Intersections)

# 2023 ROAD BOND PROGRAM PROJECTS

## Precinct 3 - Commissioner Covey

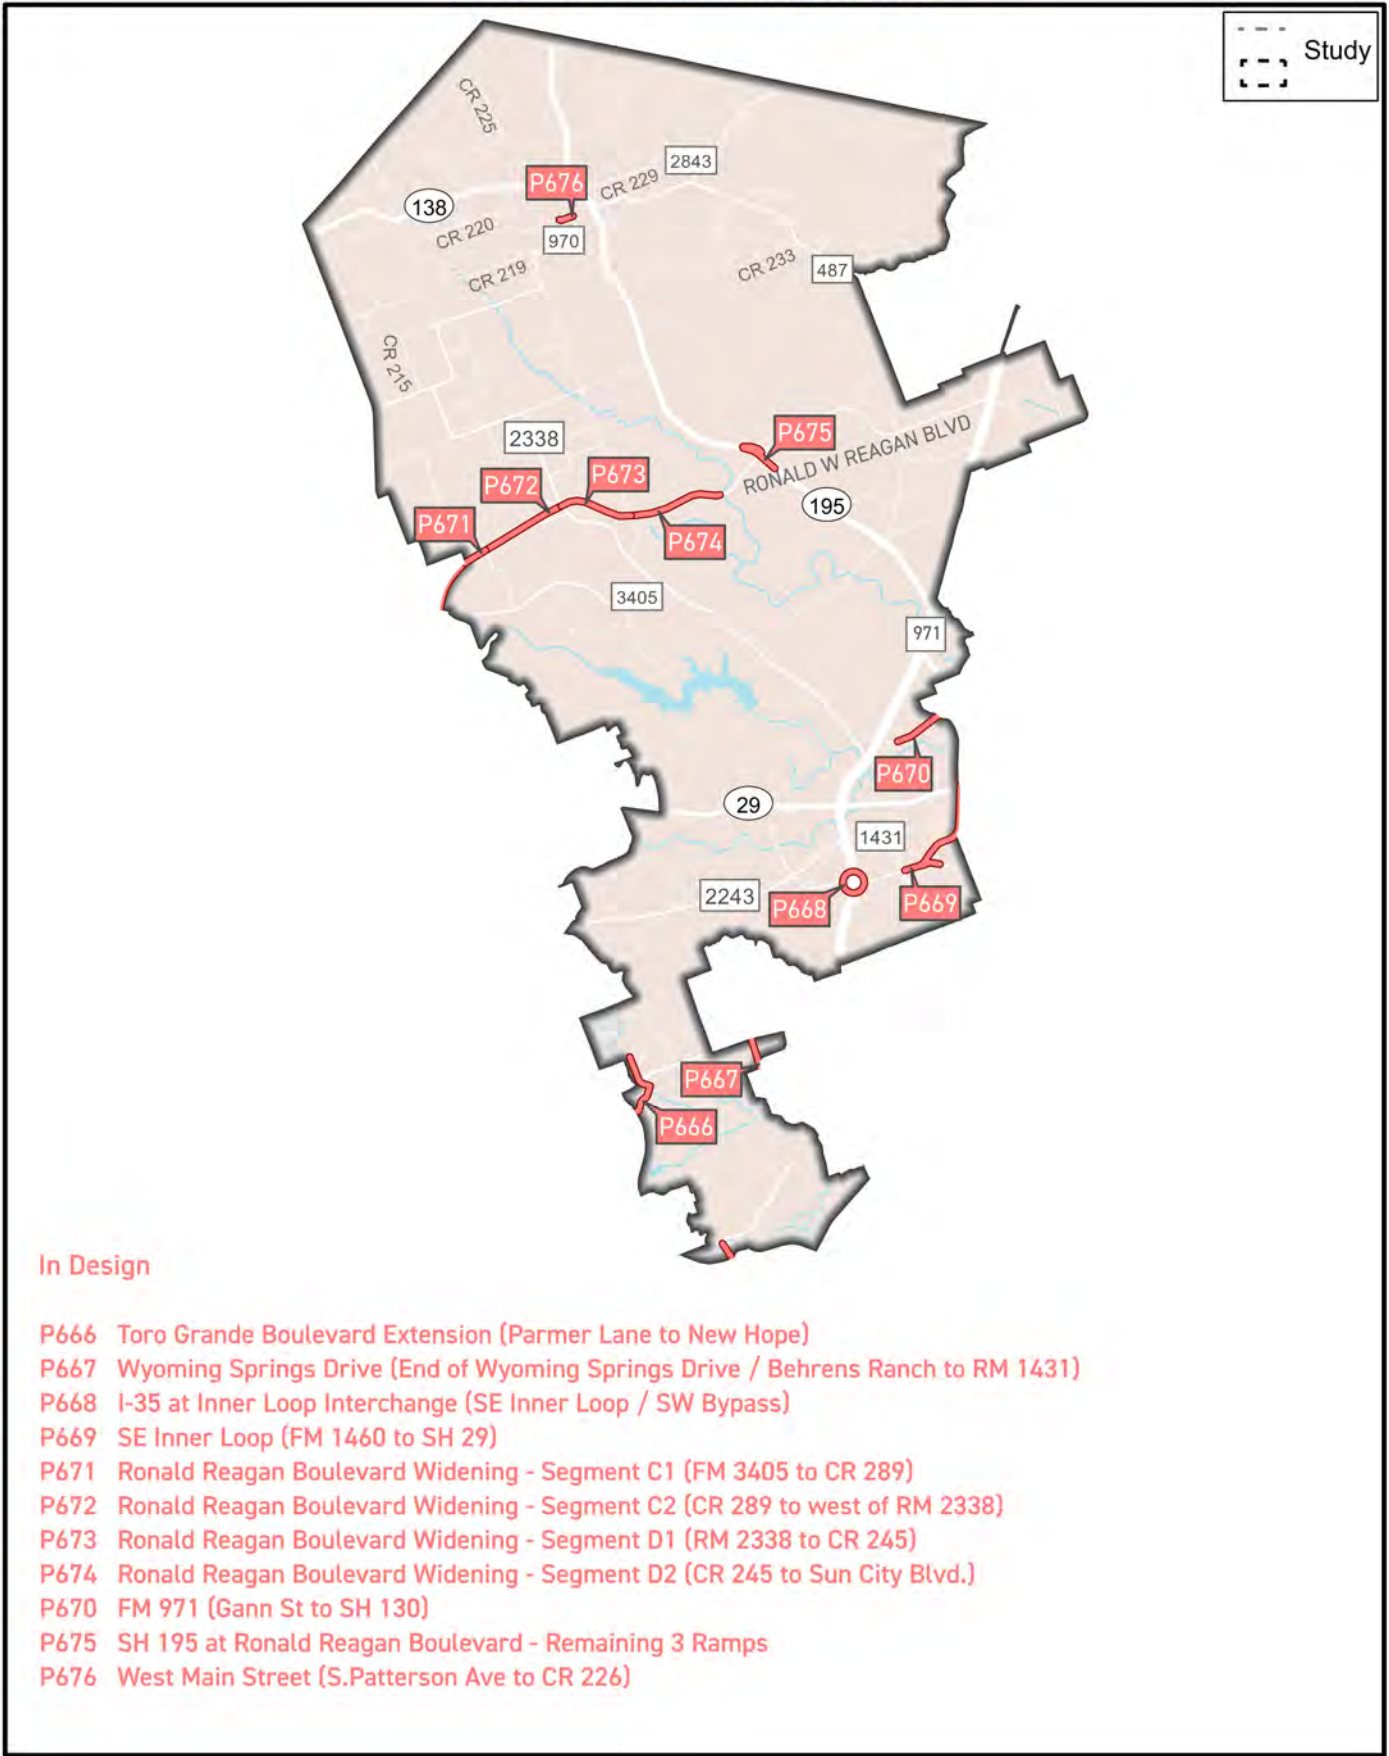

**In Design**

- P666 Toro Grande Boulevard Extension (Parmer Lane to New Hope)
- P667 Wyoming Springs Drive (End of Wyoming Springs Drive / Behrens Ranch to RM 1431)
- P668 I-35 at Inner Loop Interchange (SE Inner Loop / SW Bypass)
- P669 SE Inner Loop (FM 1460 to SH 29)
- P671 Ronald Reagan Boulevard Widening - Segment C1 (FM 3405 to CR 289)
- P672 Ronald Reagan Boulevard Widening - Segment C2 (CR 289 to west of RM 2338)
- P673 Ronald Reagan Boulevard Widening - Segment D1 (RM 2338 to CR 245)
- P674 Ronald Reagan Boulevard Widening - Segment D2 (CR 245 to Sun City Blvd.)
- P670 FM 971 (Gann St to SH 130)
- P675 SH 195 at Ronald Reagan Boulevard - Remaining 3 Ramps
- P676 West Main Street (S.Patterson Ave to CR 226)

**Project Name: CR 111 Westinghouse Road**  
**Project No. 22IFB39**

Original Contract Price = \$21,024,332.88

Letting	Award	Notice To Proceed	Begin Work	Substantial Completion	Completion Certificate	Total Bid Days	Days Added	Total Days	
12/15/2021	1/11/2022	1/20/2022	1/30/2022	3/21/2024		700		700	
Invoice Number	Beginning Date	Ending Date	Days Charged	Current Invoice	Invoiced Total	Current Retainage	Total Retainage	% (\$) Used	% Time Used
1	2/1/2022	2/28/2022	28	\$142,149.86	\$142,149.86	\$15,794.43	\$15,794.43	1	4
2	3/1/2022	3/31/2022	31	\$1,624,724.26	\$1,766,874.12	\$180,524.92	\$196,319.35	9	8
3	4/1/2022	4/30/2022	30	\$1,286,121.32	\$3,052,995.44	\$142,902.37	\$339,221.72	15	13
4	5/1/2022	5/31/2022	31	\$1,110,146.62	\$4,163,142.06	\$123,349.64	\$462,571.36	21	17
5	6/1/2022	6/30/2022	30	\$482,208.08	\$4,645,350.14	\$53,578.66	\$516,150.02	23	21
6	7/1/2022	7/31/2022	31	\$787,719.86	\$5,433,070.00	\$87,524.44	\$603,674.46	27	26
7	8/1/2022	8/31/2022	31	\$822,906.88	\$6,255,976.88	\$91,434.10	\$695,108.56	31	30
8	9/1/2022	9/30/2022	30	\$1,707,686.45	\$7,963,663.33	\$189,742.92	\$884,851.48	39	35
9	10/1/2022	10/31/2022	31	\$1,107,286.40	\$9,070,949.73	\$123,031.82	\$1,007,883.30	45	39
10	11/1/2022	11/30/2022	30	\$518,917.48	\$9,589,867.21	\$57,657.50	\$1,065,540.80	47	43
11	12/1/2022	12/31/2022	31	\$1,285,779.15	\$10,875,646.36	-\$493,138.36	\$572,402.44	51	48
12	1/1/2023	1/31/2023	31	\$620,120.59	\$11,495,766.95	\$32,637.93	\$605,040.37	54	52
13	2/1/2023	2/28/2023	28	\$846,149.01	\$12,341,915.96	\$44,534.15	\$649,574.52	58	56
14	3/1/2023	3/31/2023	31	\$639,962.65	\$12,981,878.61	\$33,682.25	\$683,256.77	61	61
15	4/1/2023	4/30/2023	30	\$717,084.56	\$13,698,963.17	\$37,741.29	\$720,998.06	64	65
16	5/1/2023	5/31/2023	31	\$661,601.87	\$14,360,565.04	\$34,821.15	\$755,819.21	67	69
17	6/1/2023	6/30/2023	30	\$591,898.92	\$14,952,463.96	\$31,152.58	\$786,971.79	70	74
18	7/1/2023	7/31/2023	31	\$555,320.94	\$15,507,784.90	\$29,227.41	\$816,199.20	72	78
19	8/1/2023	8/31/2023	31	\$451,231.96	\$15,959,016.86	\$23,749.06	\$839,948.26	74	82
20	9/1/2023	9/30/2023	30	\$371,656.43	\$16,330,673.29	\$19,560.86	\$859,509.12	76	87
21	10/1/2023	10/31/2023	31	\$230,597.40	\$16,561,270.69	\$12,136.71	\$871,645.83	77	91
22	11/1/2023	11/30/2023	30	\$179,598.00	\$16,740,868.69	\$9,452.52	\$881,098.35	78	95
23	12/1/2023	12/31/2023	31	\$801,573.10	\$17,542,441.79	\$42,188.06	\$923,286.41	82	100
24	1/1/2024	1/31/2024	31	\$858,054.72	\$18,400,496.51	\$45,160.77	\$968,447.18	86	104
25	2/1/2024	2/29/2024	29	\$802,470.59	\$19,202,967.10	\$42,235.30	\$1,010,682.48	90	108
26	3/1/2024	3/31/2024	21	\$482,112.32	\$19,685,079.42	\$25,374.33	\$1,036,056.81	92	111
27	4/1/2024	5/31/2024	0	\$640,577.80	\$20,325,657.22	-\$621,247.48	\$414,809.33	92	111
28	6/1/2024	6/30/2024	0	\$25,001.18	\$20,350,658.40	\$510.23	\$415,319.56	92	111

8/31/2024 Comments - Project close out in progress.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	5/3/2022	\$233,364.00	\$ 233,364.00

2 Differing in site conditions. (Unforeseeable) 2E. Miscellaneous difference in site conditions (unforeseeable) (item 9): This change order compensates the Contractor for over-excavating unsuitable material and importing embankment material from offsite that meets the requirements in the specifications. With the limited areas on the project to find suitable material it was agreed to import the required material. A Force Account item has been created to cover half of the cost of the imported material and half of the trucking. This amount is to cover this area and any other areas that may be encountered on site.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	5/3/2022	\$7,553.84	\$ 240,917.84

1B. Design Error or Omission. Other: This change order compensates the Contractor for upsize changes in 6 inlet and 1 junction box to accommodate pipe size design. The revisions affected estimate page 15, summary page 18, storm drainage pages: 149 for Inlet C-5 and C-6, page 150 for Inlets E-4 and E-5, page 151 for Inlet F-6, page 153 for Inlet I-6 and page 154 for Junction Box K.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	7/14/2022	\$20,307.20	\$ 261,225.04

1. Design Error or Omission. 1A: incorrect PS&E. This Change Order is in response to RFI 22 that updated the quantity for pay item 106-6002 OBLITERATING ABANDONED ROADWAY. The item has been recalculated and the difference is included in this Change Order to cover the actual quantity.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	7/13/2022	\$454,267.40	\$ 715,492.44

1. Design Error or omission. 1B. Other: This Change Order updates the bid item quantities that were revised in the plan set summary sheet, but not reflected in the Bid Form. The Change Order also includes pay items for 2 new items that were identified in the plans, but inadvertently left off the Bid Form.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	11/22/2022	\$41,134.66	\$ 756,627.10

1. Design Error or Omission. 1B. Other. The existing section of the roadway in front of Gateway School was constructed prior to the project letting. This portion of the roadway was to remain in place and the proposed roadway was to tie into it. The contractor constructed around this portion of the roadway so that the tie-ins would work with the current plan design. 1B. Other. This Change Order also adds items for flowable fill and concrete dissipaters at the culvert outfalls.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
06	11/22/2022	\$24,159.20	\$ 780,786.30

2. Differing Site Conditions: (Unforeseeable) 2J. Other: While clearing the ROW, 4 water wells were encountered. This Change Order provides payment to the Contractor for having the plugging and abandoning four (4) wells, by a licensed water well company. Upon completion of the well abandonment, plugging reports will be filed.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
07	12/14/2022	\$28,440.00	\$ 809,226.30

1B. Design Error or Omission. 1B. Other: This Change Order provides additional items to the Contract for adjusting an existing headwall, wingwalls and adding concrete rail along an existing culvert that is to remain in place. Due to the height of the existing culvert, the proposed roadway can not be built to the proposed width. Raising the headwall and constructing the rail will allow for the roadway portion to be constructed to the proposed width. This rail will mirror the existing rail along the upstream portion of the existing culvert.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
08	12/14/2022	\$276,200.00	\$ 1,085,426.30

4B. Third Party Accommodation. Third party requested work: MBC Development has requested additional sleeves to be installed across CR 111 for their future development on both sides of the roadway. The Developer Agreement has been amended to reflect the change and the Developer has funded Williamson County for this additional work.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
09	4/25/2023	\$14,282.00	\$ 1,099,708.30

1. Design Error or Omission. 1B Other: This Change Order compensates the contractor for relocating the existing service line to tie into the new meter location. The meter was relocated outside of the new ROW per the plans, but the plans did not show a service line connection for the residence back in at this location. Per the ILA, the County must, at its own expense, pay all cost related to the relocation of Jonah's water lines.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
10	6/6/2023	\$39,507.50	\$ 1,139,215.80

2E. Differing in Site Conditions. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order compensates the contractor for removing and replacing the existing concrete driveway at the Valero gas station as well as removing the sidewalk that is in conflict with the proposed roadway widening.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
11	8/22/2023	\$81,433.12	\$ 1,220,648.92

6 Untimely ROW/Utilities 6C: Utilities Not Clear: This Change Order compensates the contractor for relocating the existing 12-inch City of Georgetown water line that is in conflict with the culvert a Driveway 1. The water line is being relocated between the proposed box culvert and the ROW along the north side of the project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
12	1/9/2024	\$303,603.61	\$ 1,524,252.53

6C. Utilities not clear. This Change Order adds an item to the contract for inefficient work and delays the contractor experienced due to the utilities not being cleared throughout the project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
13	6/25/2024	15,975.61	1,540,228.14

1B. Design Error or Omission. Other. This Change Order addresses the need for low fill post, concrete footing, and a driveway terminal section not accounted for in the plans. This Change order also addresses the incorrect called out sign post that were installed per plan. 2I. Differing Site Conditions. Additional safety needs. This Change Order compensates the contractor for upsizing the stop signs at the new 4-way intersection. 4B. Third Party Accommodation. Third party requested work. Eliminated the striping and created a right turn lane on northbound FM 1460 at CR 111 per TxDOT.

---

Adjusted Price = \$22,564,561.02



**Project Name: CR 245 Reconstruction**  
**Project No. 23IFB12**

Original Contract Price = \$6,969,195.21

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/6/2022	12/13/2022	2/1/2023	2/10/2023	12/14/2023		423		423	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u> <u>Used</u>	<u>% Time</u> <u>Used</u>
1	2/10/2023	2/28/2023	19	\$143,464.59	\$143,464.59	\$15,940.51	\$15,940.51	3	4
2	3/1/2023	3/31/2023	31	\$355,908.11	\$499,372.70	\$39,545.35	\$55,485.86	9	12
3	4/1/2023	4/30/2023	30	\$378,182.90	\$877,555.60	\$42,020.32	\$97,506.18	16	19
4	5/1/2023	5/31/2023	31	\$541,611.28	\$1,419,166.88	\$60,179.03	\$157,685.21	26	26
5	6/1/2023	6/30/2023	30	\$438,431.06	\$1,857,597.94	\$48,714.56	\$206,399.77	35	33
6	7/1/2023	7/31/2023	31	\$1,157,295.20	\$3,014,893.14	\$128,588.36	\$334,988.13	56	41
7	8/1/2023	8/31/2023	31	\$1,149,398.96	\$4,164,292.10	-\$115,814.86	\$219,173.27	74	48
8	9/1/2023	9/30/2023	30	\$601,990.01	\$4,766,282.11	\$31,683.68	\$250,856.95	84	55
9	10/1/2023	10/31/2023	31	\$97,202.52	\$4,863,484.63	\$5,115.92	\$255,972.87	86	62
10	11/1/2023	11/30/2023	30	\$544,037.17	\$5,407,521.80	\$28,633.54	\$284,606.41	96	70
11	12/1/2023	1/31/2024	14	\$128,644.67	\$5,536,166.47	\$6,770.77	\$291,377.18	98	70
12	2/1/2024	2/29/2024	0	\$231,946.39	\$5,768,112.86	-\$173,660.59	\$117,716.59	99	73
13	3/1/2024	3/31/2024	0	\$48,401.14	\$5,816,514.00	\$987.78	\$118,704.37	100	73
14	4/1/2024	5/31/2024	0	\$18,980.23	\$5,835,494.23	\$387.35	\$119,091.72	100	73
15	6/1/2024	7/31/2024	0	\$62,720.74	\$5,898,214.97	-\$59,513.79	\$59,577.93	100	73
16	8/1/2024	8/31/2024	0	\$53,283.93	\$5,951,498.90	-\$59,577.93	\$0.00	100	73

8/31/2024 Comments - Close-out process under way.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	8/22/2023	20,980.10	20,980.10

1. Design Error or Omission. 1B. Other: This Change Order compensates the contractor for removing a portion of a structure that encroaches the new ROW. 2. Differing in Site Conditions: (Unforeseeable) 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order addresses karst features that were encountered while excavating to subgrade south of Smokestack Ln. The karst features were closed per SWCA and TCEQ recommendations.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	8/22/2024	-1,038,676.43	-1,017,696.33

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order provides the final balancing for the overruns/underruns of contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans. This Change Order also adds an item for additional guardrail steel posts.

**Adjusted Price = \$5,951,498.88**

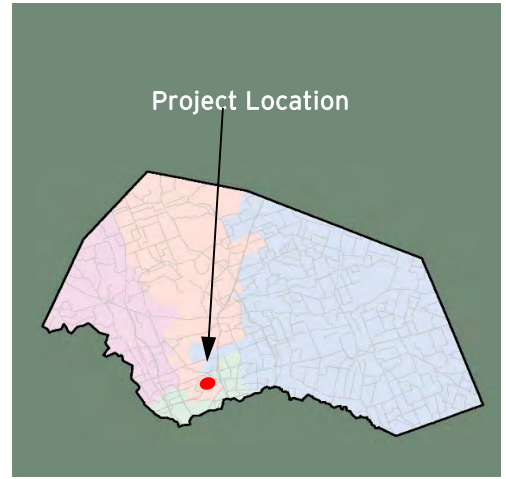

**Corridor H/Sam Bass Road  
(RM 1431 to Wyoming Springs Drive)**

**Project Length: 2.578 Miles**  
**Roadway Classification: Urban Minor Arterial**

**Project Schedule: March 2023 - Fall 2025**  
**Estimated Construction Cost: \$33.8 Million**



**AUGUST 2024 IN REVIEW**

8/2/24: Cash Construction continued installation of the Round Rock 42-inch water line between Tonkawa Trail and Wyoming Springs. Subcontractor Alpha Paving paved Great Oaks Drive on the north side of Sam Bass Road.

8/9/24: Cash graded and completed the northbound section of Sam Bass Road and switched traffic to the new roadway section. PEC’s contractor worked between Thousand Oaks and Walsh Drive.

8/16/24: Cash continued processing flexible base on the westbound section of Sam Bass Road between Thousand Oaks Drive and Mayfield Drive. Subcontractor Ranger Excavation continued roadway excavation between Thousand Oaks and Mayfield Drive.

8/23/24: Cash continued installation of the BCMUD 12-inch water line between Walsh Ranch Boulevard and Tonkawa Trail.

8/30/24: Cash continued placing flexible base throughout the project. Subcontractor Ranger Excavation continued roadway excavation and haul off at various locations throughout the project.



**Design Engineer: K Friese**  
**Contractor: Cash Construction**  
**Construction Observation:  
Tracy Cooper, HNTB**

**Williamson County  
Road Bond Program**



**Project Name: Corridor H/Sam Bass Road**  
**Project No. 23IFB8**

Original Contract Price = \$36,145,959.00

Letting	Award	Notice To Proceed	Begin Work	Substantial Completion	Completion Certificate	Total Bid Days	Days Added	Total Days
12/20/2022	1/13/2023	3/13/2023	3/23/2023			911		911

Invoice Number	Beginning Date	Ending Date	Days Charged	Current Invoice	Invoiced Total	Current Retainage	Total Retainage	% (\$)	% Time
1	4/1/2023	4/30/2023	30	\$21,095.55	\$21,095.55	\$2,343.95	\$2,343.95	0	3
2	5/1/2023	5/31/2023	31	\$511,459.79	\$532,555.34	\$56,828.87	\$59,172.82	2	7
3	6/1/2023	6/30/2023	30	\$1,024,886.41	\$1,557,441.75	\$113,876.26	\$173,049.08	5	10
4	7/1/2023	7/31/2023	31	\$148,136.40	\$1,705,578.15	\$16,459.60	\$189,508.68	6	13
5	8/1/2023	8/31/2023	31	\$915,201.56	\$2,620,779.71	\$101,689.06	\$291,197.74	9	17
6	9/1/2023	9/30/2023	30	\$510,079.42	\$3,130,859.13	\$56,675.50	\$347,873.24	10	20
7	10/1/2023	10/31/2023	31	\$900,115.81	\$4,030,974.94	\$100,012.86	\$447,886.10	13	23
8	11/1/2023	11/30/2023	30	\$731,394.97	\$4,762,369.91	\$81,266.11	\$529,152.21	16	27
9	12/1/2024	12/31/2024	31	\$241,049.16	\$5,003,419.07	\$26,783.24	\$555,935.45	16	30
10	1/1/2024	1/31/2024	31	\$412,213.73	\$5,415,632.80	\$45,801.53	\$601,736.98	18	34
11	2/1/2024	2/29/2024	29	\$986,810.97	\$6,402,443.77	\$109,645.66	\$711,382.64	21	37
12	3/1/2024	3/31/2024	31	\$909,406.35	\$7,311,850.12	\$101,045.15	\$812,427.79	24	40
13	4/1/2024	4/30/2024	30	\$1,012,728.40	\$8,324,578.52	\$112,525.38	\$924,953.17	27	43
14	5/1/2024	5/31/2024	31	\$990,023.58	\$9,314,602.10	\$110,002.62	\$1,034,955.79	31	47
15	6/1/2024	6/30/2024	30	\$714,854.15	\$10,029,456.25	\$79,428.24	\$1,114,384.03	33	50
16	7/1/2024	7/31/2024	31	\$1,590,446.20	\$11,619,902.45	\$176,716.24	\$1,291,100.27	38	54

8/31/2024 Comments - Contractor continued installation of the Round Rock 42-inch water line between Great Oaks Drive and Walsh Ranch Boulevard. Cash continued installation of the BCMUD 12-inch water line between Walsh Ranch Boulevard and Tonkawa Trail. The Contractor continued processing flexible base and roadway excavation and haul off excess material at various locations throughout the project.

Change Order Number	Approved	Cost This CO	Total COs
01	6/27/2023	\$ (2,394,078.12)	\$ (2,394,078.12)


1B: Design Error or Omission. Other. This Change Order revises the earthwork quantities, BCMUD water line items and driveway quantities, per plan revisions issued after the Bid was awarded. The quantity for Item 110-6001 excavation was reduced by over 25% and the unit price is revised because it is considered a major bid item per the Contract.

Change Order Number	Approved	Cost This CO	Total COs
02	8/22/2023	\$ 5,250.00	\$ (2,388,828.12)

1B: Design Error or Omission. Other: This Change Order updates incorrect unit prices that were inadvertently used for two existing items in Change Order 1.

**Adjusted Price = \$33,757,130.88**


## 2000/2006 Road Bond Program Projects Precinct 4 - Commissioner Boles

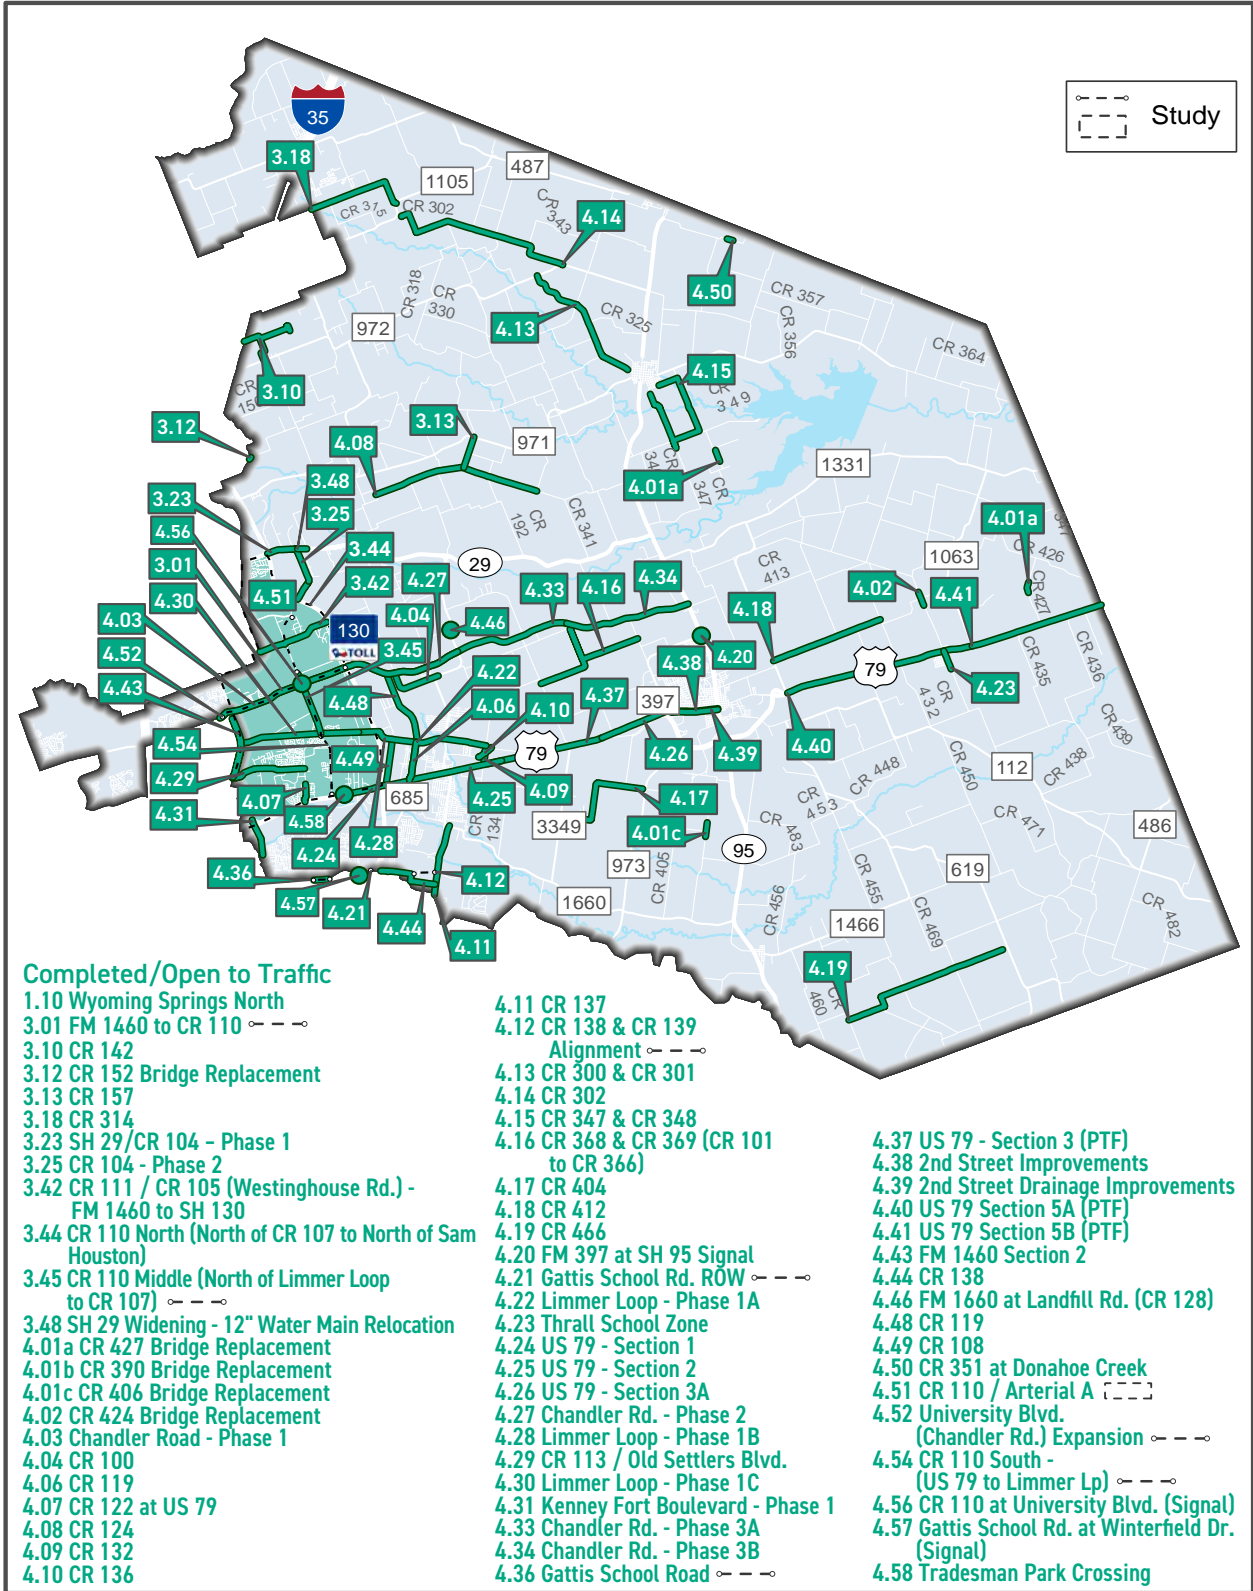



# 2013 ROAD BOND PROGRAM PROJECTS

## Precinct 4 - Commissioner Boles

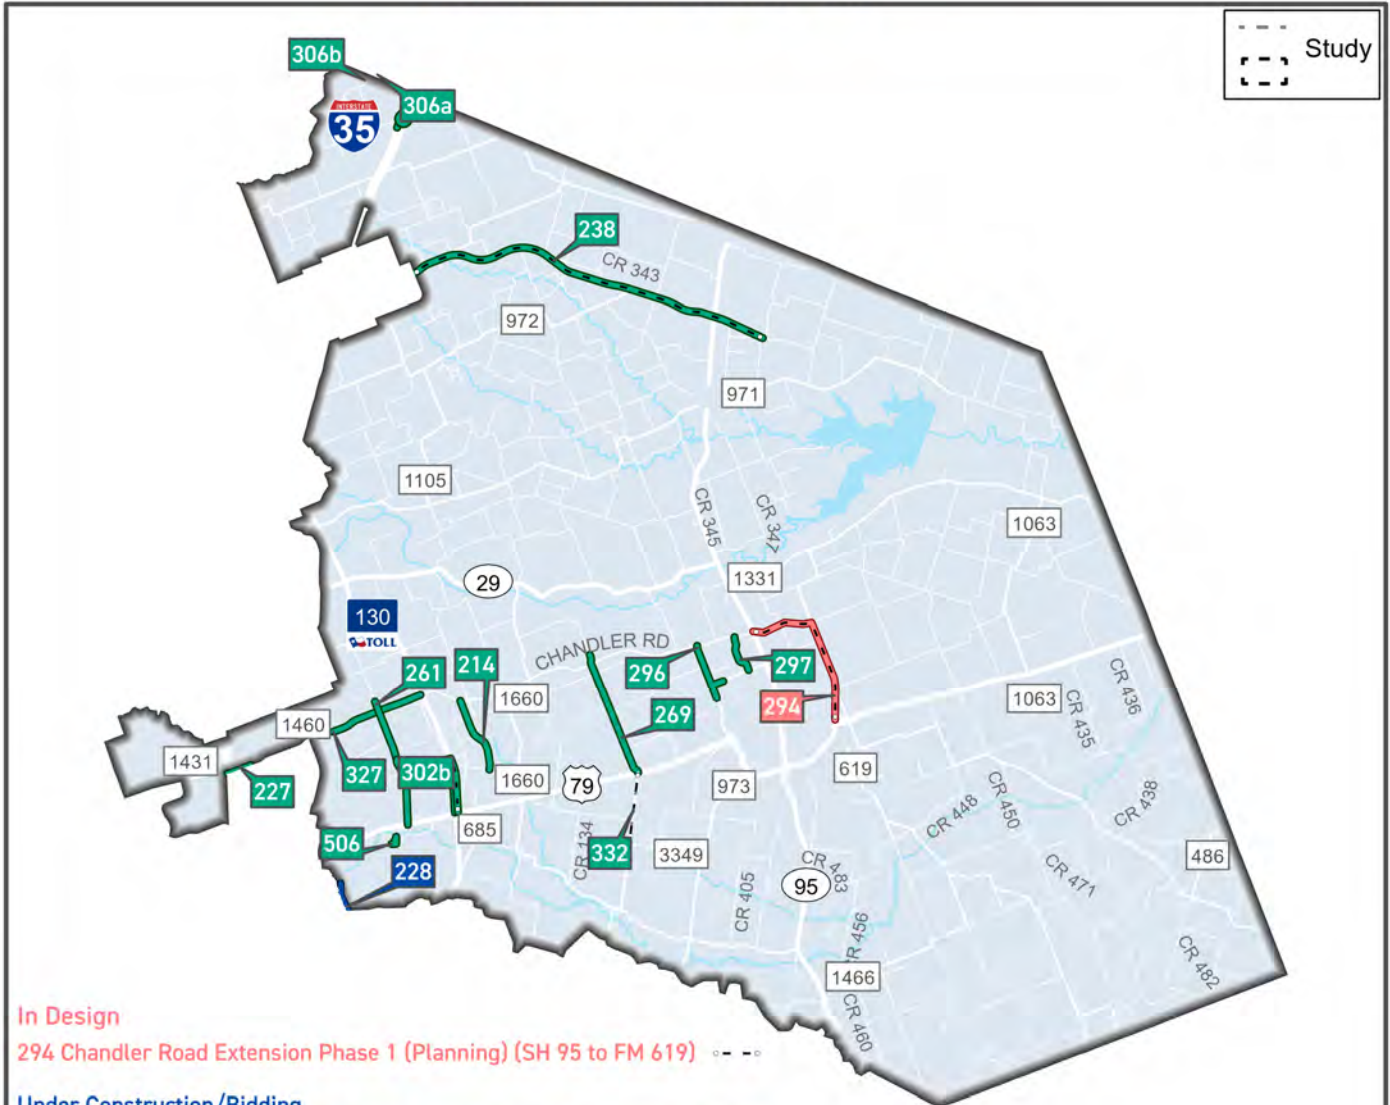

### In Design

294 Chandler Road Extension Phase 1 (Planning) (SH 95 to FM 619) - - - -

### Under Construction/Bidding


228 Kenney Fort Blvd Segments 2 and 3 (Forest Creek Boulevard to SH 45)

### Completed/Open to Traffic

- 214 CR 119 (Limmer Loop to Chandler Road)
- 227 University Boulevard Widening (IH 35 to Sunrise Road)
- 238 Ronald Reagan Boulevard Extension Planning (IH 35 to SH 95) - - - -
- 269 CR 101 (US 79 to North of Chandler Road)
- 261 CR 110 Middle (Limmer Loop to CR 107)
- 260 CR 110 South (US 79 to Limmer Loop)
- 296 CR 366 Widening (Chandler Road to Carlos G. Parker Boulevard)
- 297 East Williamson County Park Road / Bill Pickett Trail (Carlos Parker Boulevard to Chandler Road)
- 302a SH 130 Frontage Roads Phase 3 (Southbound Frontage Road US 79 to Limmer Loop)
- 302b SH 130 Traffic Study - - - -
- 306a Relocation of 48" Williamson County Regional Raw Waterline - Line A
- 306b CR 305 at IH 35 Bridge Replacement
- 327 University Boulevard (Chandler Road) Expansion (FM 1460 to SH 130)
- 332 FM 3349/US 79 Interchange (US 79 to CR 404) - - - -
- 506 Oak Bluff and Greenfield Drainage Improvements

# 2019 ROAD BOND PROGRAM PROJECTS

## Precinct 4 - Commissioner Boles

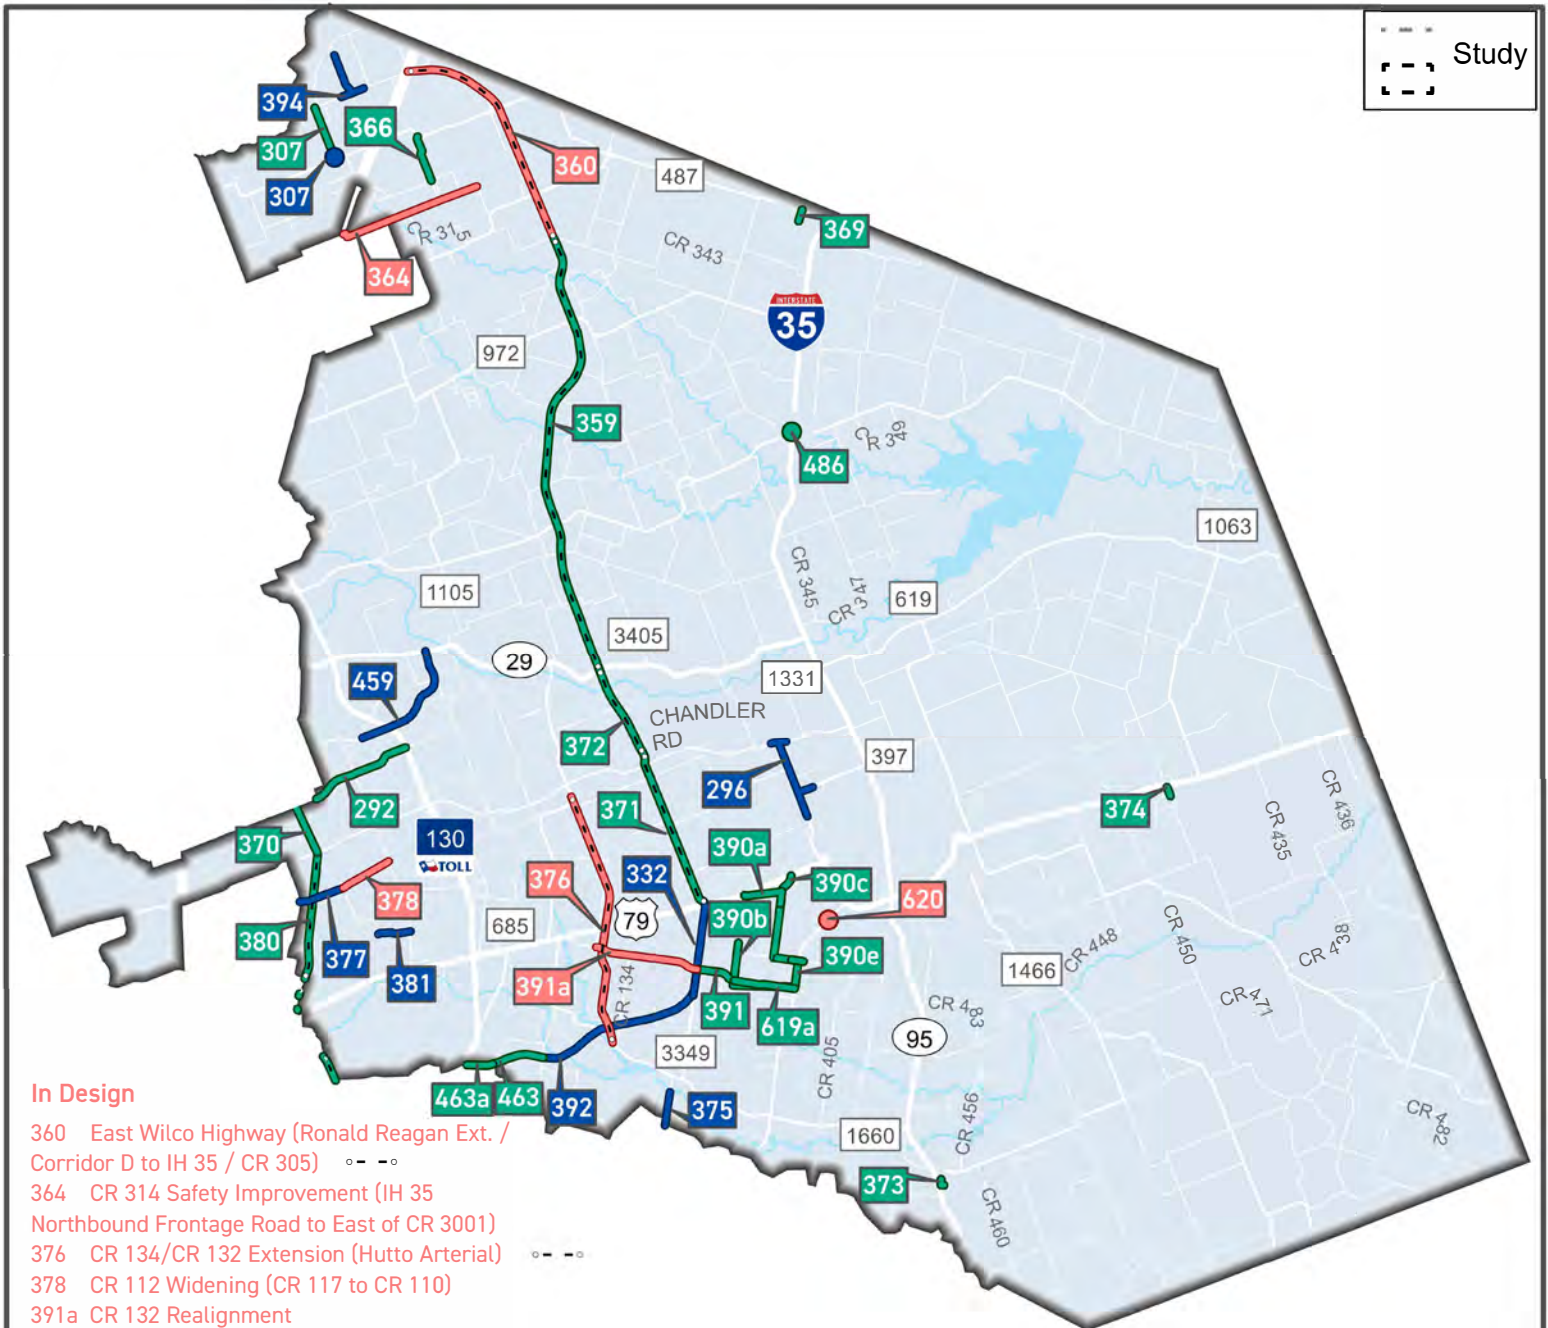

### In Design

- 360 East Wilco Highway (Ronald Reagan Ext. / Corridor D to IH 35 / CR 305) - - - -
- 364 CR 314 Safety Improvement (IH 35 Northbound Frontage Road to East of CR 3001)
- 376 CR 134/CR 132 Extension (Hutto Arterial) - - - -
- 378 CR 112 Widening (CR 117 to CR 110)
- 391a CR 132 Realignment
- 620 FM 973 at Taylor High School Signal

### Under Construction/Bidding

- 296 CR 366 (Chandler Road to Carlos G Parker Boulevard Northwest)
- 307 Bud Stockton Extension Traffic Signal at FM 487
- 332 East Wilco Highway (FM 3349/US 79 Interchange) (US 79 to CR 404)
- 375 CR 129 (South of Brushy Creek to North of the South Williamson County Line)
- 377 CR 112 Widening (FM 1460/A.W. Grimes to CR 117)
- 381 Old Settlers Boulevard (North Red Bud Lane/CR 122 to CR 110)
- 392 East Wilco Highway (Southeast Loop Segment 2, Phase 1) (CR 137 to CR 404)
- 459 Corridor C / SH 29 Bypass (Sam Houston Avenue at Patriot Way to SH 29)

### Completed/Open to Traffic


- 292 CR111/CR105 Westinghouse (FM 1460 to SH 130)
- 307 Bud Stockton Extension (CR 305 to FM 487)
- 359 East Wilco Highway (Future SH 29 to Ronald Reagan Extension/ Corridor D) - - - -
- 366 CR 332 Realignment (South of FM 487 to North of CR 313)

- 369 Bartlett Project (Cottrell Street)
- 370 MoKan (Georgetown Inner Loop to University Boulevard)
- 371 East Wilco Highway (US 79 to Chandler Rd/Corridor B2) - - - -
- 372 East Wilco Highway (Future SH 29 to Chandler Rd) - - - -
- 373 Coupland Street Project (S. Broad & Muery Streets)
- 374 Thrall Street Project - S Bounds Street - - - -
- 380 MoKan (University Boulevard to SH 45)
- 390a CR Improvements and Paving (CR 401, CR 402, CR 404)
- 390b CR 404 Hutto Water Line Realignment (Along future CR 404, from CR 404 to CR 404 at FM 973)
- 390c CR 401/CR 404 Improvements (US 79 to CR 404)
- 390e CR 404 at FM 973 (CR 404)
- 391 Samsung Highway (CR 404 Realignment) (CR 404 to FM 3349)
- 394 CR 307 Reconstruction (CR 307 North of CR 305 Jarrell)
- 463 East Wilco Highway (Southeast Loop Segment 1, Phase 1) (CR 138 to CR 137)
- 463a CR 138 Right Turn Lane at SH 130
- 486 Granger Project (Davilla Street Culvert) (Davilla Street to N Walton Street)
- 619a Samsung Highway (Future County Road) (CR 404 to FM 973)



# 2023 ROAD BOND PROGRAM PROJECTS

## Precinct 4 - Commissioner Boles

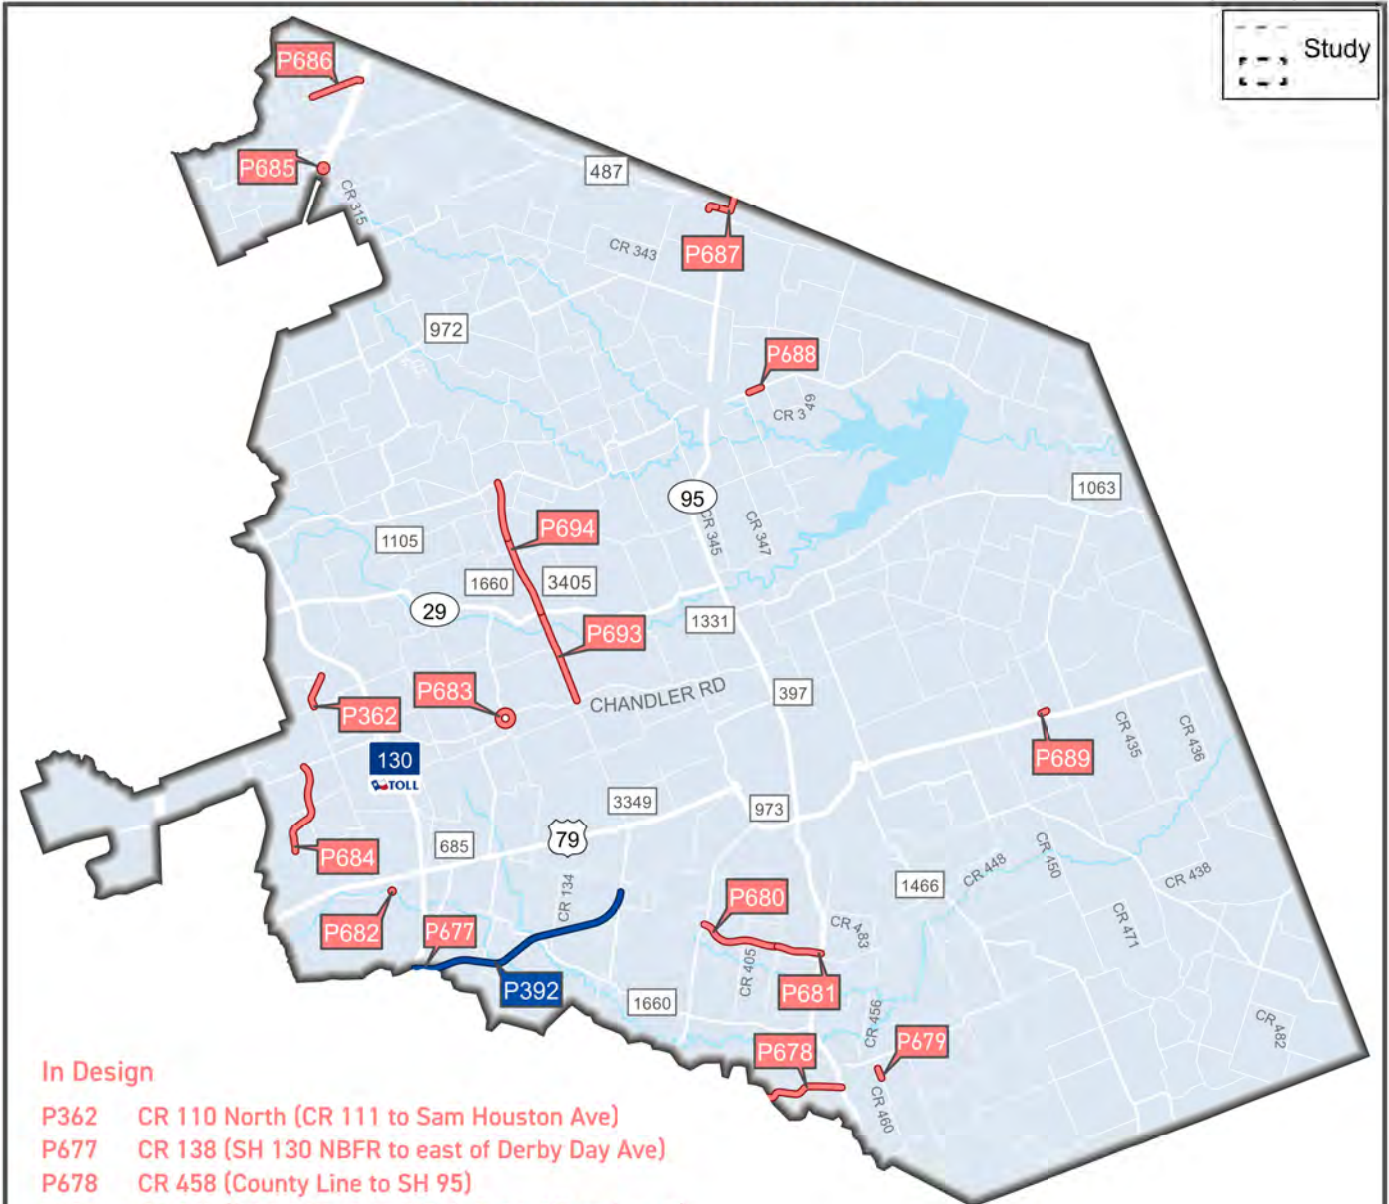

### In Design

- P362 CR 110 North (CR 111 to Sam Houston Ave)
- P677 CR 138 (SH 130 NBFR to east of Derby Day Ave)
- P678 CR 458 (County Line to SH 95)
- P679 CR 460 (future Coupland High School Turn Lanes)
- P680 Corridor A2 (FM 973 to CR 406)
- P681 Corridor A2 (CR 406 to SH 95)
- P682 CR 123 (Brushy Creek)
- P683 Chandler Road (FM 1660 Overpass)
- P684 Kenney Fort Boulevard - Segments 5 & 6 (Old Settlers Boulevard to North of University Boulevard)
- P685 Sonterra Boulevard (IH-35 Frontage Road and Sonterra Blvd Intersection)
- P686 CR 305 (IH 35 to CR 307)
- P687 Salt Lake, Brook, Front Street (Salt Lake Street to Clark Street)
- P688 FM 971 (future Granger High School Turn Lanes)
- P689 North Barker Street (CR 424 to east end of North Barker Street)
- P693 East Wilco Highway (Segment 5) (Chandler Road to SH 29)
- P694 East Wilco Highway (Segment 6) (Future SH 29 to FM 971)

### Under Construction/Bidding

- P392 East Wilco Highway ( Southeast Loop - Segment 2)(Corridor E1  
(Construction)(CR 137 south of Hutto and CR 404)

**Project Name: East Wilco Highway (Southeast Loop, Segment 1)**

**Project No. T3346**

**Original Contract Price = \$11,526,789.09**

Letting	Award	Notice To Proceed	Begin Work	Substantial Completion	Completion Certificate	Total Bid Days	Days Added	Total Days	
3/30/2021	4/27/2021	7/12/2021	7/19/2021	8/31/2023		534	24	558	
Invoice Number	Beginning Date	Ending Date	Days Charged	Current Invoice	Invoiced Total	Current Retainage	Total Retainage	% (\$) Used	% Time Used
1	7/19/2021	8/31/2021	44	\$767,411.06	\$767,411.06	\$85,267.90	\$85,267.90	7	8
2	9/1/2021	9/30/2021	30	\$328,739.28	\$1,096,150.34	\$36,526.58	\$121,794.48	10	13
3	10/1/2021	10/31/2021	31	\$221,811.16	\$1,317,961.50	\$24,645.69	\$146,440.17	12	19
4	11/1/2021	11/30/2021	30	\$278,008.69	\$1,595,970.19	\$30,889.85	\$177,330.02	15	24
5	12/1/2021	12/31/2021	31	\$331,070.23	\$1,927,040.42	\$36,785.58	\$214,115.60	18	30
6	1/1/2022	1/31/2022	31	\$624,535.89	\$2,551,576.31	\$69,392.88	\$283,508.48	23	35
7	2/1/2022	2/28/2022	28	\$352,666.85	\$2,904,243.16	\$39,185.20	\$322,693.68	27	40
8	3/1/2022	3/31/2022	31	\$815,310.79	\$3,719,553.95	\$90,590.09	\$413,283.77	34	46
9	4/1/2022	4/30/2022	30	\$741,856.71	\$4,461,410.66	\$82,428.53	\$495,712.30	41	51
10	5/1/2022	5/31/2022	31	\$625,433.98	\$5,086,844.64	\$69,492.66	\$565,204.96	46	57
11	6/1/2022	6/30/2022	30	\$498,845.27	\$5,585,689.91	\$55,427.25	\$620,632.21	51	62
12	7/1/2022	7/31/2022	31	\$521,580.90	\$6,107,270.81	\$57,953.44	\$678,585.65	56	68
13	8/1/2022	8/31/2022	31	\$672,002.44	\$6,779,273.25	\$74,666.93	\$753,252.58	62	73
14	9/1/2022	9/30/2022	30	\$936,075.41	\$7,715,348.66	\$104,008.38	\$857,260.96	70	79
15	10/1/2022	10/31/2022	31	\$851,880.44	\$8,567,229.10	-\$406,354.16	\$450,906.80	74	84
16	11/1/2022	11/30/2022	30	\$625,071.12	\$9,192,300.22	\$32,898.48	\$483,805.28	80	90
17	12/1/2022	12/31/2022	31	\$290,510.48	\$9,482,810.70	\$15,290.02	\$499,095.30	82	95
18	1/1/2023	1/31/2023	31	\$55,998.20	\$9,538,808.90	\$2,947.27	\$502,042.57	83	101
19	2/1/2023	2/28/2023	28	\$161,924.00	\$9,700,732.90	\$8,522.32	\$510,564.89	84	106
20	3/1/2023	3/31/2023	31	\$291,588.78	\$9,992,321.68	\$15,346.78	\$525,911.67	86	111
21	4/1/2023	4/30/2023	30	\$160,641.77	\$10,152,963.45	\$8,454.83	\$534,366.50	88	117
22	5/1/2023	5/31/2023	31	\$79,909.01	\$10,232,872.46	\$4,205.73	\$538,572.23	98	122
23	6/1/2023	6/30/2023	30	\$355,060.22	\$10,587,932.68	\$18,687.38	\$557,259.61	92	128
24	7/1/2023	7/31/2023	31	\$61,540.97	\$10,649,473.65	\$3,239.00	\$560,498.61	92	133
25	8/1/2023	8/31/2023	31	\$316,670.90	\$10,966,144.55	\$16,666.89	\$577,165.50	95	139
26	9/1/2023	9/30/2023	0	\$84,593.72	\$11,050,738.27	\$4,452.30	\$581,617.80	96	139
27	10/1/2023	10/31/2023	0	\$8,808.52	\$11,059,546.79	\$463.61	\$582,081.41	96	139

8/31/2024 Comments - Closeout is underway.

Change Order Number	Approved	Cost This CO	Total COs
01	8/3/2021	\$ 148,710.35	\$ 148,710.35

6B. This Change Order adds the installation of barbed wire fence and gates along the north and south sides of the right of way on the Wolfe property. The Contractor will not be able to start work until the fence is installed. Twenty four (24) days are being added to the contract to compensate the contractor for this impact.

Change Order Number	Approved	Cost This CO	Total COs
02	10/4/2022	\$73,007.39	\$221,717.74

2C. Differing site conditions (Unforeseeable). New development (conditions changing after PS&E completed): This Change Order documents various changes to the contract related to new developer and Church driveways on the west end of the project. 3F. County Convenience. Additional work desired by the County: In addition to the driveways, the bridge rail was changed along the bridge to a more appealing look. 1B. Design Error or Omission. Other: Additional excavation was needed in Pond 21 to create more volume and line EA had to be adjusted for optimum flow along Wall 4.

Change Order Number	Approved	Cost This CO	Total COs
03	2/28/2023	\$177,807.62	399,525.36

1A. Incorrect PS&E. This Change Order replaces the SGT and MBGF with Crash Cushion Attenuators on the proposed eastbound lane at both bridges due to them not being able to be installed per plan because of the post locations being in the MSE rock backfill. 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order also compensates the contractor for replacing a portion of an existing concrete driveway that needed to be removed to install the 48in RCP on Line B35.

Change Order Number	Approved	Cost This CO	Total COs
04	3/28/2023	156,231.96	555,757.32

2. Differing Site Conditions (Unforeseeable) 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9): This Change Order is adding items to the Contract that have been previously paid for under the existing Force Account line item.

Change Order Number	Approved	Cost This CO	Total COs
05	7/20/2023	1,093,581.24	1,649,338.56

1. Design Error or Omission. 1A: Incorrect PS&E. This Change Order addresses quantity revisions with the earthwork, roadway and various other bid items. The original quantities were incorrect in the Bid documents. The Engineer of Record re-calculated the quantities and provided revised numbers.

Change Order Number	Approved	Cost This CO	Total COs
06	9/27/2023	-1,015,961.92	633,376.64

3M. County Convenience. Other. Due to the existing utility conflicts impeding the remaining construction, this Change Order will remove all remaining work from Phases 2-4 from the project.

**Adjusted Price = \$12,160,165.73**



**Project Name: CR 401 Reconstruction Project**  
**Project No. 22IFB57**

Original Contract Price = \$12,673,200.94

Letting	Award	Notice To Proceed	Begin Work	Substantial Completion	Completion Certificate	Total Bid Days	Days Added	Total Days
3/11/2022	3/22/2022	4/21/2022	5/2/2022	7/7/2023	6/12/2024	505	-70	435

Invoice Number	Beginning Date	Ending Date	Days Charged	Current Invoice	Invoiced Total	Current Retainage	Total Retainage	% (\$) Used	% Time Used
1	4/14/2022	4/21/2022	0	\$541,350.00	\$541,350.00	\$60,150.00	\$60,150.00	5	0
2	4/22/2022	5/31/2022	30	\$213,264.25	\$754,614.25	\$23,696.03	\$83,846.03	6	7
3	6/1/2022	7/1/2022	31	\$1,394,793.70	\$2,149,407.95	\$154,977.08	\$238,823.11	17	14
4	7/2/2022	7/31/2022	30	\$690,418.59	\$2,839,826.54	\$76,713.17	\$315,536.28	23	21
5	8/1/2022	8/31/2022	31	\$276,688.62	\$3,116,515.16	\$30,743.18	\$346,279.46	25	28
6	9/1/2022	9/30/2022	30	\$784,682.38	\$3,901,197.54	\$87,186.93	\$433,466.39	31	35
7	10/1/2022	10/31/2022	31	\$776,738.57	\$4,677,936.11	\$86,304.29	\$519,770.68	37	42
8	11/1/2022	11/30/2022	30	\$875,684.24	\$5,553,620.35	\$97,298.25	\$617,068.93	44	49
9	12/1/2022	12/31/2022	31	\$422,000.74	\$5,975,621.09	\$46,888.97	\$663,957.90	48	56
10	1/1/2023	1/31/2023	31	\$616,120.11	\$6,591,741.20	\$68,457.79	\$732,415.69	52	63
11	2/1/2023	2/28/2023	28	\$598,319.58	\$7,190,060.78	\$66,479.95	\$798,895.64	57	70
12	3/1/2023	3/31/2023	31	\$603,951.86	\$7,794,012.64	\$67,105.76	\$866,001.40	62	77
13	4/1/2023	4/30/2023	30	\$945,657.20	\$8,739,669.84	-\$406,018.78	\$459,982.62	66	84
14	5/1/2023	5/31/2023	31	\$1,082,327.54	\$9,821,997.38	\$56,964.61	\$516,947.23	74	91
15	6/1/2023	6/30/2023	30	\$1,195,677.91	\$11,017,675.29	\$62,930.42	\$579,877.65	83	98
16	7/1/2023	7/31/2023	7	\$760,493.51	\$11,778,168.80	\$40,025.97	\$619,903.62	89	99
17	8/1/2023	8/31/2023	0	\$16,945.32	\$11,795,114.12	\$891.86	\$620,795.48	89	99
18	9/1/2023	9/30/2023	0	\$543,436.59	\$12,338,550.71	-\$368,988.32	\$251,807.16	90	99
19	10/1/2023	10/31/2023	0	\$156,673.75	\$12,495,224.46	\$3,197.42	\$255,004.58	91	99
20	11/1/2023	11/30/2023	0	\$335,156.29	\$12,830,380.75	\$6,839.93	\$261,844.51	94	99
21	12/1/2023	12/31/2023	0	\$309,329.80	\$13,139,710.55	\$6,312.85	\$268,157.36	96	99
22	1/1/2024	1/31/2024	0	\$53,097.83	\$13,192,808.38	\$1,083.63	\$269,240.99	96	99
23	2/1/2024	2/29/2024	0	\$38,782.60	\$13,231,590.98	\$791.48	\$270,032.47	96	99
24	3/1/2024	3/31/2024	0	\$130,741.40	\$13,362,332.38	\$2,668.19	\$272,700.66	97	99
25	4/1/2024	4/30/2024	0	\$511.56	\$13,362,843.94	\$10.44	\$272,711.10	98	99

8/31/2024 Comments - Closeout process is underway.

Change Order Number	Approved	Cost This CO	Total COs
01	9/15/2022	\$ 13,315.52	\$ 13,315.52

3G. County Convenience. Compliance requirements of new laws and/or policies. Revised the pavement section within the US 79 TxDOT ROW to meet their requirements and revised some signal phasing/timing at the proposed intersection of US 79 and CR 401.

Change Order Number	Approved	Cost This CO	Total COs
02	9/20/2022	\$ 414,400.00	\$ 427,715.52

4B. Third Party Accommodation. Third party requested work. This Change Order reduces the Contract Time by 70 days, from 505 Calendar days to 435 Calendar Days with a maximum incentive cap. This acceleration in the Contract Time is necessary, in order to meet the County's project delivery deadline of 7/31/2023.

Change Order Number	Approved	Cost This CO	Total COs
03	10/5/2022	\$ 214,351.37	\$ 642,066.89

3F. County Convenience. Additional work desired by the County. This Change Order changes the City of Taylor water line pipe material from ductile iron to PVC. This is necessary, due to the availability of materials.

Change Order Number	Approved	Cost This CO	Total COs
04	2/28/2023	\$ 188,826.95	\$ 830,893.84

2G. Differing in site conditions. Unadjusted Utility (Unforeseeable) This Change Order adds new items to the Contract to adjust the existing 16in City of Taylor water line on the north side of US 79 which is in conflict with the proposed pavement and ditch cuts. 4B. Third Party Requested Work. An additional 6in line and fire hydrant assembly are being added at the request of the City of Taylor.

Change Order Number	Approved	Cost This CO	Total COs
05	8/22/2023	\$ -	\$ 830,893.84

2. Differing Site Conditions. 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9) This Change Order compensates the Contractor for additional work to the Jonah water line that had to be rerouted due to a conflict with the bore pit for the City of Taylor water line. A Force Account line item has been created to cover the cost of the repair to the Jonah water line.

Change Order Number	Approved	Cost This CO	Total COs
06	12/19/2023	\$399,968.56	\$ 1,230,862.40

2E. Miscellaneous difference in site conditions (unforeseeable). Due to changing conditions in the field, certain items required quantity adjustments. 2I. Additional safety needs (unforeseeable). Additional small signs were added for safety concerns near the railroad crossing. This Change Order also adds items for crash cushion repairs needed due to the damage that occurred during construction.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
07	1/30/2024	\$137,831.49	\$ 1,368,693.89

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order adjusts quantities in the Contract due to unforeseen conditions that were identified in the field. This Change Order also adds additional items to the Contract for work being performed in and around the UPRR ROW per requirements.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
08R	6/18/2024	71,380.34	1,440,074.23

1. Design Error or Omission. 1B Other: This Change Order adds items to the Contract to compensate the contractor for extended overhead, stand-by time, and additional mobilization cost due to additional UPRR jack & bore requirements. This Change Order also adds an item to install, flush, remove, and return a fire hydrant to the City of Taylor. 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9): This Change Order also provides the final balancing for the overruns/underruns of Contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
09	6/18/2024	-151,545.26	1,288,528.97

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9): This Change Order provides the final balancing for the overruns/underruns of Contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans. This Change Order also adds a quantity for Extended Overhead due to a UPRR delay.

---

Adjusted Price = \$13,961,729.91

---

**Project Name: Samsung Highway (Future County Road) (CR 404 to FM 973)**

**Project No. 22IFB126**

Original Contract Price = \$11,289,929.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
7/12/2022	7/19/2022	8/5/2022	8/15/2022	9/5/2023		413		413	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	8/15/2022	9/27/2022	44	\$415,099.80	\$415,099.80	\$46,122.20	\$46,122.20	4	11
2	9/28/2022	10/31/2022	34	\$1,256,916.42	\$1,672,016.22	\$139,657.38	\$185,779.58	17	19
3	11/1/2022	11/30/2022	30	\$529,743.42	\$2,201,759.64	\$58,860.38	\$244,639.96	22	26
4	12/1/2022	12/31/2022	31	\$196,710.30	\$2,398,469.94	\$21,856.70	\$266,496.66	24	34
5	1/1/2023	1/31/2023	31	\$942,884.78	\$3,341,354.72	\$104,764.98	\$371,261.64	34	41
6	2/1/2023	2/28/2023	28	\$895,707.90	\$4,237,062.62	\$99,523.10	\$470,784.74	43	48
7	3/1/2023	3/31/2023	31	\$2,066,773.05	\$6,303,835.67	\$229,641.45	\$700,426.19	64	55
8	4/1/2023	4/30/2023	30	\$1,637,718.64	\$7,941,554.31	-\$282,449.65	\$417,976.54	76	63
9	5/1/2023	5/31/2023	31	\$1,177,188.70	\$9,118,743.01	\$61,957.30	\$479,933.84	88	70
10	6/1/2023	7/31/2023	61	\$1,026,783.27	\$10,145,526.28	\$54,041.23	\$533,975.07	98	85
11	8/1/2023	8/31/2023	31	\$78,532.37	\$10,224,058.65	\$4,133.28	\$538,108.35	98	92
12	9/1/2023	9/30/2023	5	\$339,420.15	\$10,563,478.80	-\$322,527.15	\$215,581.20	98	94
13	10/1/2024	4/26/2024	0	\$70,667.06	\$10,634,145.86	\$1,442.19	\$217,023.39	99	94

8/31/2024 Comments - Close-out process is underway.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	1/24/2023	41,260.00	\$ 41,260.00

1B. Design Error or Omission. Other: This Change Order adds two items to the Contract for installing a 4' x 2' box culvert (EE) and related wingwalls/headwalls. The work was shown in the plans but not included in the bid tab. This Change Order also removes SET (TY 1) (S=5ft)(HW=3FT) (6:1) (C) item. The work was removed from the plans but the item was left in the bid tab. These plan revisions were made prior to bidding due to outstanding items on the TxDOT permit for the work at the FM 973 tie-in.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	7/18/2023	83,559.50	\$ 124,819.50

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order adds quantities to existing items due to unexpected changes in field conditions, causing overruns on the project. The excavation and embankment quantities had to be adjusted, due to the existing elevations at the west tie-in. The 18-inch and 36-inch drill shafts needed to be extended to ensure the shafts had proper embedment into stable material.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	6/25/2024	-470,934.99	-346,115.49

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order provides the final balancing for the overruns/underruns of Contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans. This Change Order also revises quantities for the added left turn lane to the Samsung Driveway, as well as adds additional erosion control items.



Adjusted Price = \$10,943,813.51

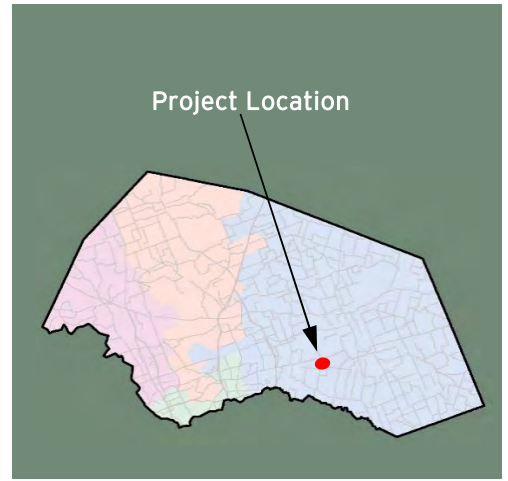

**East Wilco Highway (FM 3349 at US 79)  
(FM 3349 from US 79 to CR 404 and new interchange on US 79 at FM 3349 and CR 101)**

**Project Length: 4.108 Miles  
Roadway Classification: Rural Major Collector**

**Project Schedule: October 2022 - Summer 2025 (Roadwork)  
Estimated Construction Cost: \$84 Million**

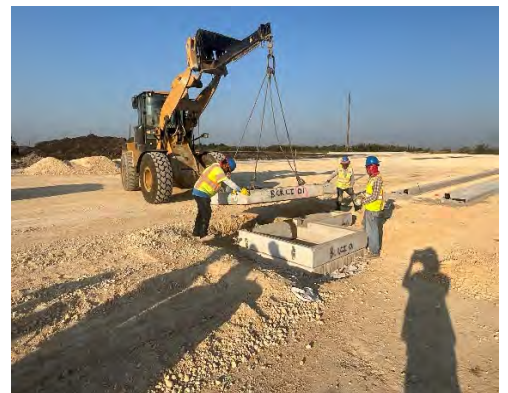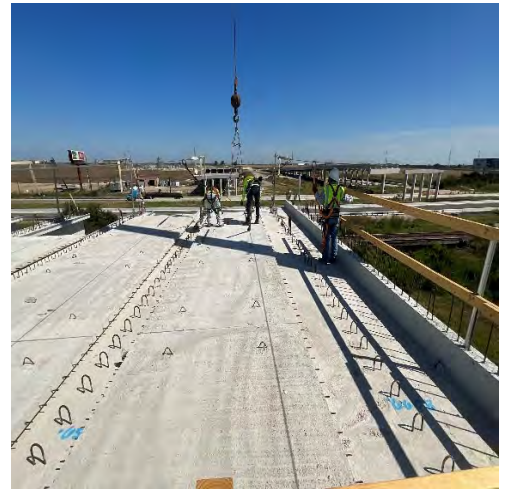

## **AUGUST 2024 IN REVIEW**

8/2/24: James Construction Group (JCG) continued cutting ditches and drainage swales in the median at the south end of the project. JCG continued to work on culvert headwalls and setting curb inlets.

8/9/24: JCG continued to work on culvert headwalls and setting curb inlets along the southbound frontage road. Subcontractor Austin Traffic Signal installed conduit for illumination along the southbound frontage road.

8/16/24: JCG continued hauling off material from the southbound frontage road drainage swale excavation. Subcontractor Lone Star Paving placed prime and began paving asphalt for the southbound frontage road.

8/23/24: JCG began lime stabilization along the northbound frontage road north of US 79. Subcontractor Patin began working on tie-ins from the new water line to the properties along the project.

8/30/24: JCG continued to set deck panels on the northbound frontage road bridge.

**Design Engineer: HDR  
Contractor: James Construction  
Construction Observation:  
Asif Mirzazada, HNTB**

**Williamson County  
Road Bond Program**



**Project Name: East Wilco Highway (FM 3349 at US 79)**

**Project No. 22IFB139**

Original Contract Price = \$81,941,038.13

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
8/24/2022	9/26/2022	10/6/2022	10/17/2022			1394		1394

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$ Used)</u>	<u>% Time Used</u>
1	10/18/2022	11/25/2022	39	\$755,690.77	\$755,690.77	\$0.00	\$0.00	1	2
2	11/26/2022	12/25/2022	30	\$5,128,955.59	\$5,884,646.36	\$0.00	\$0.00	7	0
3	12/26/2022	1/25/2023	31	\$1,448,580.10	\$7,333,226.46	\$0.00	\$0.00	9	7
4	1/26/2023	2/25/2023	31	\$1,272,882.90	\$8,606,109.36	\$0.00	\$0.00	10	9
5	2/26/2023	3/25/2023	28	\$2,922,159.15	\$11,528,268.51	\$0.00	\$0.00	14	11
6	3/26/2023	4/25/2023	31	\$1,453,458.85	\$12,981,727.36	\$0.00	\$0.00	15	14
7	4/26/2023	5/25/2023	30	\$1,672,497.88	\$14,654,225.24	\$0.00	\$0.00	17	16
8	5/26/2023	6/25/2023	31	\$3,188,150.58	\$17,842,375.82	\$0.00	\$0.00	21	18
9	6/26/2023	7/25/2023	30	\$2,251,767.13	\$20,094,142.95	\$0.00	\$0.00	24	20
10	7/26/2023	8/25/2023	31	\$2,453,925.93	\$22,548,068.88	\$0.00	\$0.00	27	22
11	8/26/2023	9/30/2023	36	\$4,580,138.95	\$27,128,207.83	\$0.00	\$0.00	32	25
12	10/1/2023	10/25/2023	25	\$3,017,528.73	\$30,145,736.56	\$0.00	\$0.00	36	27
13	10/26/2023	11/25/2023	31	\$2,172,558.80	\$32,318,295.36	\$0.00	\$0.00	38	29
14	11/26/2023	12/25/2023	30	\$1,638,115.30	\$33,956,410.66	\$0.00	\$0.00	40	31
15	12/26/2023	1/25/2024	31	\$4,633,009.82	\$38,589,420.48	\$0.00	\$0.00	46	33
16	1/26/2024	2/25/2024	31	\$4,487,381.38	\$43,076,801.86	\$0.00	\$0.00	51	36
17	2/26/2024	3/25/2024	29	\$3,973,465.64	\$47,050,267.50	\$0.00	\$0.00	56	38
18	3/26/2024	4/25/2024	31	\$1,993,459.10	\$49,043,726.60	\$0.00	\$0.00	58	40
19	4/26/2024	5/25/2024	30	\$1,414,938.37	\$50,458,664.97	\$0.00	\$0.00	60	42
20	5/26/2024	6/25/2024	31	\$3,026,457.98	\$53,485,122.95	\$0.00	\$0.00	64	44
21	6/26/2024	7/25/2024	30	\$832,712.20	\$54,317,835.15	\$0.00	\$0.00	65	46

8/31/2024      Comments -      The Contractor continued construction of the southbound U-turn on the north side of US 79. The Contractor continued forming and pouring backless inlets and continued installation of rock riprap behind backless inlets and culverts along the northbound and southbound frontage roads. The Contractor continued placing concrete for bridge deck on the southbound frontage road and tying rebar for the northbound frontage road bridge south of the RR tracks. Subcontractor ATS poured concrete for various illumination pole drill shafts and ground boxes throughout the project. The Contractor completed the tie-ins from the new water line to the properties throughout the project.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	4/25/2023	925,354.41	925,354.41

3. County Convenience. 3L Revising safety work/measures desired by the County: This Change Order provides funds to compensate the contractor for installing safety improvements on US 79 until the permanent overpasses are built. By installing these traffic control measures the drivers traveling north bound on FM 3349 can no longer proceed straight or make a left turn at the US 79 intersection. The same will apply for traffic traveling south on CR 101. Drivers will need to make a right turn on US 79

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	4/25/2023	82,000.00	1,007,354.41

3. County Convenience. 3L Revising safety work/measures desired by the County: The original bid item 36-inch Ductile Iron Pipe has long lead time of material procurement and is not readily available. Contractor proposed two options with shorter lead time to the City of Hutto as alternatives. City of Hutto has approved option 2, which is 36-inch PVC DR 18 pipe as an alternative with \$82,000 increase in cost to the current item and allows contractor to procure material quicker. The cost of this material change is 100% reimbursable by the City of Hutto.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	7/20/2023	195,302.81	1,202,657.22

3. County Convenience. 3F Additional work desired by the County: This Change Order compensates the contractor for installing one steel utility sleeve casing 24 inches in diameter on FM 3349 at station 421+00.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	8/8/2023	-472,492.20	730,165.02

3. County Convenience. 4D Other "Deletion of work requested by the City of Hutto": This Change Order eliminates City of Hutto 16-inch water main line relocations project and 50 LF of 16-inch water line relocation under City of Hutto water line casing project from the original scope of work. The omission of work was requested by the City of Hutto. The cost for restocking of the ordered material and any other related fee is 100% reimbursable by the City of Hutto.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
05	0/14/23	-5,274.97	724,890.05

5. Contractor Convenience. 5E Other: This Change Order is to revise the Stone Riprap material cost due to a material substitution request from the contractor. James Construction proposed material that has a specific gravity below the Contract requirements but has been accepted by TxDOT in other projects. The EOR approved the use of this material and recommended a reduction in price. This Change Order will result in a cost savings for the proposed material. This Change Order also adds new items to the Contract to pay the Contractor for additional work that was originally paid under the Force Account Line item.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
06	10/20/2023	130,053.00	854,943.05
3. County Convenience. 3F Additional work desired by the County: This Change Order compensates the contractor for upsizing 562 LF of 12-inch PVC pipe and fittings to 16-inch PVC pipe for the Jonah waterline project due to increased demand. The decision to upsize the pipe was at Jonah's request and will be 100% funded by the Jonah Water Special Utility District.			
07	10/20/2023	661,031.30	1,515,974.35
3F. Additional work desired by the County : This Change Order compensates the contractor for installing southbound frontage road right turn lane at FM 3349 for City of Hutto Mega Site. This work was requested by the City of Hutto and is 100% reimbursable by the City of Hutto.			
08	10/20/2023	327,321.48	1,843,295.83
1. Design Error or Omission. 1B. Other: This Change Order compensates the contractor for installation of 280 linear feet of 36-inch Ductile Iron (DI) pipe for City of Hutto water line project, instead of the previously specified 36-inch PVC pipe. This adjustment is required for the 48-inch bored steel casing under FM 3349 and the transition to a 56-inch casing for the open cut section. This modification was requested by and is 100% reimbursable by the City of Hutto.			
09	1/30/2024	-368,749.53	1,474,546.30
5. Contractor Convenience. 5A Contractor exercises option to change the traffic control plan: This Change Order revises the as-bid Traffic Control Plan (TCP) and construction phasing of the FM 3349 project. The modified TCP allows the Contractor to work on both, the North Bound and South Bound Frontage Roads simultaneously. The changes to the TCP and construction phasing do not impact the project's completion date and results in savings on several contract items.			
10	1/30/2024	67,965.30	1,542,511.60
4. Third Party Accommodation. 4B. Third party requested work: This Change Order compensates the Contractor for installing 390 LF of 4-inch steel casing with 1.5" HDPE water service line and fittings for the Jonah waterline project on FM 3349 at station 475+50. This work was requested by the Jonah Water Special Utility District and is 100% reimbursed by the Jonah Water Special Utility District.			
11	2/1/2024	271,902.72	1,814,414.32
3. County Convenience. 3F. Additional work desired by the County: This Change Order provides compensation to the Contractor for the installation of a 24-inch Steel Encasement Sleeve spanning 470 linear feet in the Jonah water line project on FM 3349 at station 426+51. The sleeve is part of the Williamson County real estate agreement executed during the ROW acquisition.			
12	4/16/2024	64,791.00	1,879,205.32
1. Design Error or Omission - 1A. Incorrect PS&E. 4B. Third party requested work: This Change Order provides compensation to the Contractor for modifying the length and elevation of the Jonah water line under US79 and UPRR tracks, and for abandoning the existing 2-Inch Jonah water line located within the UPRR ROW on the south side of US79.			
13	4/16/2024	82,301.65	1,961,506.97
2. Differing Site Conditions (unforeseeable) 2I. Additional safety needs: This Change Order provides compensation to the Contractor for performing pavement repairs, within the project limits, on the existing FM 3349 roadway. The repairs include fixing ruts and cracks and repairing a crash cushion and MBGF damaged by the public. This Change Order also adds new items to install additional small signs to improve safety on the CR 101 (Jughandle Road), pay for off duty police officers, and locating an existing utility line.			
14	4/16/2024	101,248.22	2,062,755.19
2C. New Development (Conditions Changing After PS&E Completed). This Change Order provides compensation to the Contractor for relocating box culvert No. 4 on the southbound frontage road, to accommodate the location of the new City of Hutto street (Spine Road). The culvert and crossover to FM 3349 were moved approximately 36ft. to the north to align with the centerline of the Spine Road.			
15	7/16/2024	24,513.18	2,087,268.37
2. Differing Site Conditions (unforeseeable). 2C. New development (conditions changing after PS&E completed). This Change Order provides compensation to the Contractor for additional construction surveying, traffic control management, and low production asphalt placement due to the different site conditions on driveway No. 5 of the northbound frontage road.			
16	7/16/2024	35,324.07	2,122,592.44
2. Differing Site Conditions (unforeseeable) 2I. Additional safety needs: This Change Order provides compensation to the Contractor for performing pavement repairs, within the project limits, on the existing US 79 eastern turnaround roadway. The repairs include removal of existing failed asphalt surface and flex base areas and replacing it with full depth hot mixed asphalt.			
17	7/16/2024	11,849.07	2,134,441.51
1. Design Error or Omission 1A. Incorrect PS&E: This Change Order provides compensation to the Contractor for abandoning the water well and removing the pump house, ancillary pipes and fittings, electrical power supply, concrete slab, and performing dirt work within the project right-of-way (ROW) and the Jonah SUD water line easement. The roadway plans do not show the well, and the Jonah water line plans include a note stating, "County to coordinate abandonment of structure with property owner." However, a pay item was not included in the original Contract.			

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
18	8/13/2024	18,623.43	2,153,064.94


2. Differing Site Conditions. 2G Unadjusted Utility (unforeseeable): This Change Order compensates the Contractor for modifying the jacked & bored and open trench sections of the Jonah 36-in steel encased water line on Line A. During construction, a newly installed gas line along the northside of US 79 was found to be in conflict with the proposed water line. To clear the conflict, the jacked & bored section of the water line was lowered by 5 ft. This change created the need for additional shoring and material handling, and fittings to return the water line to its original elevation before continuing with the open cut section. To mitigate the cost, Jonah SUD provided revised plan sheets reducing the length of the jacked & bore section and increasing the length of the open cut section. The unused steel casing and spacers were delivered to Jonah SUD for future use.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
19	8/13/2024	9,869.00	2,162,933.94

1. Design Error or Omission. 1A Incorrect PS&E : This Change Order compensates the Contractor for replacing the bridge blister anchor bolts for the illumination poles on the northbound and southbound bridges. The as-bid plan set specified the incorrect type of base plate and anchor bolts for the bridge mounted poles. The Contractor submitted an RFI proposing to use the specified base plates with the correct type of anchor bolts. The Engineer of Record (EOR) reviewed the request and agreed with the Contractor's proposal. As a result of this change, 27 previously approved and fabricated anchor bolt sets, will be replaced with the correct type for the specified illumination poles. The supplier did not give the Contractor the option to pay a re-stocking fee for the original anchor bolts. Therefore, 27 anchor bolts will be delivered to Wilco maintenance yard to be used in future projects.

---

Adjusted Price = \$84,103,972.07

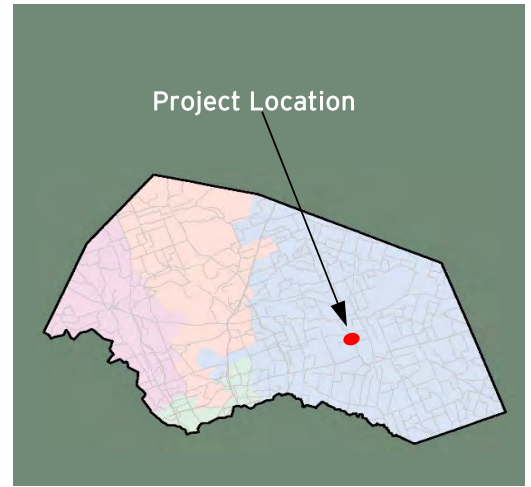

**CR 366 Reconstruction  
(Chandler Road to Carlos G. Parker Boulevard)**

**Project Length: 2.751 Miles  
Roadway Classification: Rural Arterial**

**Project Schedule: January 2023 - Summer 2024  
Estimated Construction Cost: \$17.8 Million**



**AUGUST 2024 IN REVIEW**

8/2/24: James Construction (JCG) formed and poured multiple concrete driveways on the east side of CR 366. Subcontractor Roadway Specialties completed installing small signs.

8/9/24: JCG continued to grade topsoil on the sides of CR 366 and FM 397. Subcontractor Texas Materials began paving the final surface of asphalt along Chandler Road.

8/16/24: Subcontractor Roadway Specialties began installing mailboxes throughout the project. Subcontractor Texas Materials began paving the final surface of asphalt on CR 366.

8/23/24: JCG formed and poured concrete driveways along Chandler Road at the east end of the project. Subcontractor Fuquay placed seed and soil blankets on the south side of FM 397.

8/30/24: JCG switched traffic to the final configuration on 8/23/24. Subcontractor DIJ striped words and arrows throughout project.



Design Engineer: Garver  
Contractor: James Construction  
Construction Observation:  
Chuck Evans, HNTB

Williamson County  
Road Bond Program





**Project Name: CR 366 Reconstruction (Chandler Road to Carlos G. Parker Boulevard)**

**Project No. 22IFB138**

Original Contract Price = \$17,694,262.46

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
8/31/2022	9/28/2022	12/27/2022	1/6/2023			515		515	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	1/6/2023	2/28/2023	54	\$1,184,919.53	\$1,184,919.53	\$131,657.73	\$131,657.73	7	10
2	3/1/2023	3/31/2023	31	\$220,649.15	\$1,405,568.68	\$24,516.57	\$156,174.30	9	17
3	4/1/2023	4/30/2023	30	\$195,624.79	\$1,601,193.47	\$21,736.09	\$177,910.39	10	22
4	5/1/2023	5/31/2023	31	\$540,591.96	\$2,141,785.43	\$60,065.77	\$237,976.16	13	28
5	6/1/2023	6/30/2023	30	\$1,603,804.24	\$3,745,589.67	\$178,200.47	\$416,176.63	23	34
6	7/1/2023	7/31/2023	31	\$781,944.84	\$4,527,534.51	\$86,882.76	\$503,059.39	28	40
7	8/1/2023	8/31/2023	31	\$1,589,668.07	\$6,117,202.58	\$176,629.79	\$679,689.18	38	46
8	9/1/2023	9/30/2023	30	\$933,910.69	\$7,051,113.27	\$103,767.85	\$783,457.03	44	52
9	10/1/2023	10/31/2023	31	\$448,939.28	\$7,500,052.55	\$49,882.14	\$833,339.17	47	58
10	11/1/2023	11/30/2023	30	\$314,298.57	\$7,814,351.12	\$34,922.07	\$868,261.24	49	64
11	12/1/2023	12/31/2023	31	\$413,086.23	\$8,227,437.35	\$45,898.47	\$914,159.71	45	70
12	1/1/2024	1/31/2024	31	\$452,008.26	\$8,679,445.61	\$50,223.14	\$964,382.85	54	76
13	2/1/2024	2/29/2024	29	\$653,498.36	\$9,332,943.97	\$72,610.92	\$1,036,993.77	58	82
14	3/1/2024	3/31/2024	31	\$1,806,457.71	\$11,139,401.68	-\$450,709.47	\$586,284.30	66	88
15	4/1/2024	4/30/2024	30	\$1,982,213.76	\$13,121,615.44	\$104,327.04	\$690,611.34	77	93
16	5/1/2024	5/31/2024	31	\$493,857.95	\$13,615,473.39	\$25,992.52	\$716,603.86	80	99
17	6/1/2024	6/30/2024	30	\$581,362.25	\$14,196,835.64	\$30,598.02	\$747,201.88	84	105
18	7/1/2024	7/31/2024	31	\$412,312.68	\$14,609,148.32	\$21,700.66	\$768,902.54	86	111

8/31/2024 James Construction Group switched traffic to the final configuration on 8/23/24. Subcontractor Fuquay placed soil blankets on the sides of FM 397. Subcontractor DIJ striped words and arrows throughout project. The Ribbon Cutting Ceremony is scheduled for 9/18/24.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	6/6/2023	\$ 11,562.50	\$ 11,562.50

1A. Design Error or Omission. Incorrect PS&E. : This change order adds the installation of the construction exits along CR 366 and FM 397 Carlos G Parker to access to the project site. The construction entrances or exits are to provide a stable pathway to keep the mud sediment off the public roads and improve safety.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	12/12/2023	\$ 82,015.80	\$ 93,578.30

2I: Additional safety needs (unforeseeable): This Change Orders provides funds to compensates the Contractor to implement a full closure of CR 366 until the completion of the project. The full closure is needed due to the severe rutting and pavement failures the road experienced after construction started. Williamson County and the City of Taylor agreed to close the road to through traffic and implement a detour route to improve the safety of the traveling public and facilitate the construction of the new road. 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9): This Change Order also creates new contract items for mowing and potholing to locate unmarked utilities within the project limits.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	5/7/2024	71,050.63	164,628.93

2I. Additional safety needs (unforeseeable): This Change Order compensates the Contractor for various items paid under Force Account to address required additional safety improvements, repairs to the existing CR 366, and potholing to locate existing fiber optic lines. 3F. Additional work desired by the County: This Change Order also compensates the Contractor for widening a driveway on CR 369, replacing unsuitable material on CR 366, installing an underdrain pipe, removing Oncor poles on CR 366 and FM 397, and paying off duty police officers.

**Adjusted Price = \$17,858,891.39**

**Project Name: Bud Stockton Extension (CR 305 to FM 487)**

**Project No. 23IFB13**

Original Contract Price = \$5,917,275.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/12/2022	12/20/2022	1/3/2023	2/9/2023	8/14/2023		177	6	183	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	2/1/2023	2/28/2023	16	\$173,685.65	\$173,685.65	\$19,298.41	\$19,298.41	3	9
2	3/1/2023	3/31/2023	31	\$509,598.69	\$683,284.34	\$56,622.07	\$75,920.48	13	26
3	4/1/2023	4/30/2023	30	\$596,757.76	\$1,280,042.10	\$66,306.42	\$142,226.90	25	42
4	5/1/2023	5/31/2023	31	\$935,377.65	\$2,215,419.75	\$103,930.85	\$246,157.75	43	59
5	6/1/2023	6/30/2023	30	\$493,627.50	\$2,709,047.25	\$54,847.50	\$301,005.25	52	75
6	7/1/2023	7/31/2023	31	\$1,774,451.07	\$4,483,498.32	\$197,161.23	\$498,166.48	86	92
7	8/1/2023	8/31/2023	14	\$822,967.99	\$5,306,466.31	-\$218,878.78	\$279,287.70	92	100
8	9/1/2023	9/30/2023	0	\$220,970.36	\$5,527,436.67	-\$166,482.87	\$112,804.83	98	100
9	10/1/2023	10/31/2023	0	\$27,078.46	\$5,554,515.13	\$552.62	\$113,357.45	98	100
10	11/1/2023	3/1/2024	0	\$15,204.70	\$5,569,719.83	\$310.30	\$113,667.75	99	100

8/31/2024 Comments - Awaiting vegetation establishment.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	3/7/2023	\$ 35,830.59	\$ 35,830.59

6D. Untimely ROW/Utilities. Other.: As part of the ROW Agreement, Williamson County is responsible for installing the new fence along the ROW. The Agreement was finalized after the design, so the items were not included in the bid documents. Also, temporary fence must be installed around the existing pond while the pond is being backfilled.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	8/23/2023	\$ 97,110.00	\$ 132,940.59

2. Differing Site Conditions (unforeseeable) 2E: Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order compensates the Contractor for performing full-depth repairs to the existing Bud Stockton Loop pavement prior to the 1-inch overlay of hot mix asphalt.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	2/14/2024	-292,169.97	-159,229.38

2E. Miscellaneous difference in site conditions (unforeseeable) (Item 9). This Change Order provides the final balancing for the overruns/underruns of Contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans. 2I. Additional safety needs (unforeseeable). Due to the new stop condition on FM 487, TxDot requested LED stop signs and rumble strips be installed to make a safer condition at the new all-way stop. 2J. Other: Installing a 6in sleeve for Jarrell ISD High School under their new driveway off of Bud Stockton.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
04	7/16/2024	2,905.00	-156,324.38

4.Third Party Accommodations. 4B. Third party requested work: This Change Order compensates the contractor for adding additional "T" post and tightening a portion of the newly installed fence along the Hawthorne Parcel and Wilco ROW.

**Adjusted Price = \$5,760,950.62**

**Project Name: CR 307 and CR 305**  
**Project No. 23IFB34**

Original Contract Price = \$2,796,832.80

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
2/22/2023	3/7/2023	4/7/2023	4/17/2023	2/12/2024		120	181	301

<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	4/1/2023	4/30/2023	13	\$105,372.90	\$105,372.90	\$11,708.10	\$11,708.10	5	4
2	5/1/2023	5/31/2023	31	\$78,480.00	\$183,852.90	\$8,720.00	\$20,428.10	8	15
3	6/1/2023	6/30/2023	30	\$319,844.70	\$503,697.60	\$35,538.30	\$55,966.40	22	25
4	7/1/2023	7/31/2023	31	\$298,387.80	\$802,085.40	\$33,154.20	\$89,120.60	34	35
5	8/1/2023	8/31/2023	31	\$262,632.60	\$1,064,718.00	\$29,181.40	\$118,302.00	46	45
6	9/1/2023	9/30/2023	30	\$9,900.00	\$1,074,618.00	\$1,100.00	\$119,402.00	46	55
7	10/1/2023	10/31/2023	31	\$128,916.90	\$1,203,534.90	\$14,324.10	\$133,726.10	51	65
8	11/1/2023	11/30/2023	30	\$554,425.38	\$1,757,960.28	-\$41,201.87	\$92,524.23	71	75
9	12/1/2023	12/31/2023	31	\$6,650.00	\$1,764,610.28	\$350.00	\$92,874.23	72	76
10	1/1/2024	1/31/2024	31	\$585,425.81	\$2,350,036.09	\$30,811.88	\$123,686.11	95	89
11	2/1/2024	2/29/2024	12	\$158,831.53	\$2,508,867.62	-\$72,484.73	\$51,201.38	99	100
12	3/1/2024	3/31/2024	0	\$31,267.10	\$2,540,134.72	\$638.10	\$51,839.48	100	100
13	4/1/2024	5/31/2024	0	\$27,528.48	\$2,567,663.20	-\$25,903.49	\$25,935.99	100	100
14	6/1/2024	7/31/2024	0	\$29,435.99	\$2,597,099.19	-\$25,935.99	\$0.00	100	100

8/31/2024 Comments - Project close out in progress.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	11/2/2023	\$ 10,447.50	\$ 10,447.50

2. Differing Site Conditions (unforeseeable) 2I. Additional safety needs (unforeseeable): This Change Order adds work zone pavement markings to the CR307 portion of the project. With the added amount of traffic on CR 307 due to the new school opening, the temporary pavement markings were added as an additional safety measure for the traveling public.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	2/14/2024	\$ 35,000.00	\$ 45,447.50

6C. Utilities not clear. This Change Order adds days to the contract time and increases the Barricades, signs, and traffic handling item due to the utility conflicts not being cleared by the dates stated in the Project Construction Manual.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
03	6/24/2024	-245,181.11	-199,733.61

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order provides the final balancing for the overruns/underruns of contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans.

Adjusted Price = \$2,597,099.19

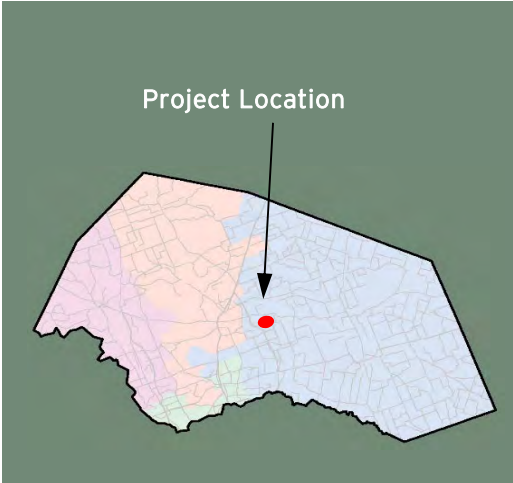

**Corridor C / SH 29 Bypass  
(Sam Houston Avenue at Patriot Way to SH 29)**

**Project Length: 2.3 Miles  
Roadway Classification: Suburban Arterial**

**Project Schedule: October 2023 - Summer 2026  
Estimated Construction Cost: \$30.5 Million**



**AUGUST 2024 IN REVIEW**

8/2/24: Capital Excavation continued setting deck panels for the SH 130 bridge and continued pouring concrete riprap at various locations throughout the project.

8/9/24: Capital poured the deck for spans 1-3 on the SH 130 bridge. Capital continued placing topsoil throughout the project.

8/16/24: Capital continued forming and pouring concrete riprap at various locations throughout the project. Capital continued processing flexible base along the SH 29 widening.

8/23/24: Capital continued forming and tying steel for spans 6-8 on the SH 130 bridge. Subcontractor ESSI continued seeding and placing erosion control blankets at various locations throughout project.

8/30/24: Capital continued placing topsoil throughout the project. Subcontractor ESSI began installing permanent small signs throughout project.



**Design Engineer: Atkins  
Contractor: Capital Excavation  
Construction Observation:  
Joseph Jones, HNTB**

**Williamson County  
Road Bond Program**





**Corridor C / SH 29 Bypass  
Project No. 23IFB67**

Original Contract Price = \$30,540,848.03

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
8/15/2023	8/22/2023	9/20/2023	9/30/2023			973		973	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>
1	9/30/2023	9/30/2023	1	\$1,397,211.48	\$1,397,211.48	\$155,245.72	\$155,245.72	5	0
2	10/1/2023	10/31/2023	31	\$1,541,032.92	\$2,938,244.40	\$171,225.88	\$326,471.60	11	3
3	11/1/2023	11/30/2023	30	\$1,838,538.26	\$4,776,782.66	\$204,282.03	\$530,753.63	17	6
4	12/1/2023	12/31/2023	31	\$2,431,249.16	\$7,208,031.82	\$270,138.79	\$800,892.42	26	10
5	1/1/2024	1/31/2024	31	\$1,078,672.93	\$8,286,704.75	\$119,852.55	\$920,744.97	30	13
6	2/1/2024	2/29/2024	29	\$2,770,832.24	\$11,057,536.99	\$307,870.25	\$1,228,615.22	40	16
7	3/1/2024	3/31/2024	31	\$1,644,580.73	\$12,702,117.72	\$182,731.19	\$1,411,346.41	46	19
8	4/1/2024	4/30/2024	30	\$3,003,806.67	\$15,705,924.39	\$333,756.30	\$1,745,102.71	57	22
9	5/1/2024	5/31/2024	31	\$1,749,723.10	\$17,455,647.49	\$194,413.68	\$1,939,516.39	63	25
10	6/1/2024	6/30/2024	30	\$3,336,725.12	\$20,792,372.61	-\$845,180.99	\$1,094,335.40	72	28
11	7/1/2024	7/31/2024	31	\$769,078.30	\$21,561,450.91	\$40,477.81	\$1,134,813.21	74	31

8/31/2024      The Contractor continued placing concrete bridge deck and forming and tying steel for future spans pours on the SH 130 bridge. The Contractor continued placing topsoil and processing flexible base in various locations throughout the project. The Contractor began installing permanent small signs and placed prime and seal coat in various locations throughout the project.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	5/2/2024	\$ 6,201.00	\$ 6,201.00

2. Differing Site Conditions (Unforeseeable) 2J. Other: This Change Order compensates the contractor for installing and removing a temporary 2-strand electric fence to maintain cattle while the Jonah water line is installed across private property.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	7/3/2024	\$ 9,568.50	\$ 15,769.50

1B. Design Error or Omission. Other.: This Change Order compensates the contractor for maintaining an existing Jonah water meter that was not accounted for in the plans.

Adjusted Price = \$30,556,617.53

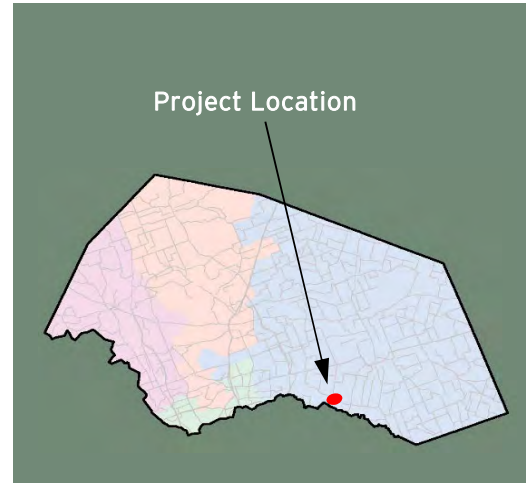

**CR 129**  
**(South of Brushy Creek to North of Williamson County Line)**

**Project Length: 0.468 Miles**  
**Roadway Classification: Rural Highway**

**Project Schedule: March 2024 - Late 2024**  
**Estimated Construction Cost: \$2.4 Million**



**AUGUST 2024 IN REVIEW**

8/2/24: Chasco fine graded the lime treated subgrade for the entire project. The contractor placed geo-grid and began processing flexible base for the entire project.

8/9/24: Chasco completed placing geo-grid and processing flexible base for the entire project. Chasco graded all driveways in preparation for asphalt paving next week.

8/16/24: Chasco continued grading all driveways in preparation for asphalt this week. Subcontractor Texas Materials placed prime, chip seal, and paved the first lift of asphalt for the entire length of the project.

8/23/24: Chasco continued placing topsoil on the front slopes of the ditches throughout the project. The contractor placed a small underdrain in the southbound CR 129 ditch line at the north end of the project.

8/30/24: Chasco began forming and pouring concrete for the safety end treatments on the driveways in the middle section of the project.



Design Engineer: Garver  
 Contractor: Chasco Constructors  
 Construction Observation:  
 Kyle McCoy, HNTB

Williamson County  
 Road Bond Program



**County Road 129  
Project No. 24IFB23**

Original Contract Price = \$2,463,313.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>		
1/17/2024	1/30/2024	2/21/2024	3/4/2024			215		215		
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>	
1	3/4/2024	3/31/2024	28	\$81,166.50	\$81,166.50	\$9,018.50	\$9,018.50	4	13	
2	4/1/2024	4/30/2024	30	\$310,646.25	\$391,812.75	\$34,516.25	\$43,534.75	18	27	
3	5/1/2024	5/31/2024	31	\$263,047.50	\$654,860.25	\$29,227.50	\$72,762.25	30	41	
4	6/1/2024	6/30/2024	30	\$231,940.35	\$886,800.60	\$25,771.15	\$98,533.40	40	55	
5	7/1/2024	7/31/2024	31	\$174,474.36	\$1,061,274.96	\$19,386.04	\$117,919.44	48	70	
8/31/2024	Comments -	The contractor finished placing HMA pavement and continued placing topsoil on the front slopes of the ditches throughout the project. Chasco continued forming and pouring concrete for driveways and the culvert safety end treatments throughout the project.								
						Adjusted Price = \$2,463,313.00				

**CR 332 Realignment  
Project No. 24IFB14**

Original Contract Price = \$2,545,345.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/5/2023	12/12/2023	2/5/2024	2/15/2024			240		240	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time</u>
1	2/5/2024	2/29/2024	15	\$535,916.70	\$535,916.70	\$59,546.30	\$59,546.30	23	6
2	3/1/2024	3/31/2024	31	\$565,245.45	\$1,101,162.15	\$62,805.05	\$122,351.35	48	19
3	4/1/2024	4/30/2024	30	\$108,512.78	\$1,209,674.93	\$12,056.98	\$134,408.33	52	32
4	5/1/2024	5/31/2024	31	\$194,134.50	\$1,403,809.43	\$21,570.50	\$155,978.83	61	45
5	6/1/2024	6/30/2024	30	\$417,247.12	\$1,821,056.55	\$46,360.79	\$202,339.62	79	57
6	7/1/2024	7/31/2024	22	\$553,976.59	\$2,375,033.14	-\$153,869.56	\$48,470.06	95	66

8/31/2024      Comments - Awaiting vegetation establishment. Chasco continued vegetative watering.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	4/24/2024	\$ 17,175.00	\$ 17,175.00

4. Third Party Accommodation 4B: Third party requested work: While performing the pre-shutdown for the Sonterra water line it was determined that Sonterra had a valve that would not close. Sonterra requested that the contractor replace the damaged valve as well as relocate an existing air release that was in conflict with the new tie-in.

Adjusted Price = \$2,562,520.00



**CR 138 Right Turn Lane at SH 130**  
**Project No. 24IFB19**

Original Contract Price = \$1,748,938.75

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>	
12/19/2023	1/9/2024	2/12/2024	2/22/2024	5/6/2024	8/26/2024	120		120	
<u>Invoice Number</u>	<u>Beginning Date</u>	<u>Ending Date</u>	<u>Days Charged</u>	<u>Current Invoice</u>	<u>Invoiced Total</u>	<u>Current Retainage</u>	<u>Total Retainage</u>	<u>% (\$)</u>	<u>% Time Used</u>
1	2/20/2024	2/29/2024	10	\$167,340.78	\$167,340.78	\$18,593.42	\$18,593.42	13	8
2	3/1/2024	3/31/2024	31	\$331,151.09	\$498,491.87	\$36,794.57	\$55,387.99	38	34
3	4/1/2024	4/30/2024	30	\$744,553.73	\$1,243,045.60	\$82,728.19	\$138,116.18	96	59
4	5/1/2024	5/31/2024	6	\$153,988.33	\$1,397,033.93	-\$109,605.28	\$28,510.90	99	64
5	6/1/2024	6/30/2024	0	\$11,568.62	\$1,408,602.55	\$236.09	\$28,746.99	100	64
6	7/1/2024	8/31/2024	0	\$33,746.99	\$1,442,349.54	-\$28,746.99	\$0.00	100	64

8/31/2024 Comments - The project was granted Final Acceptance on 8/26/24.


<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
01	5/7/2024	\$ 29,920.92	\$ 29,920.92

3F. Additional work desired by the County. This Change Order compensates the Contractor for the installation of additional signs to the project to increase the safety along the roadway as well as addressing the roadway name change. This Change Order also adds a pedestrian handrail to increase the safety along a section of the shared use path, and adds a line item for law enforcement presence during nighttime lane closure operations at the intersection of CR 138 and SH 130.

<u>Change Order Number</u>	<u>Approved</u>	<u>Cost This CO</u>	<u>Total COs</u>
02	8/22/2024	\$ (336,510.13)	\$ (306,589.21)

2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9). This Change Order provides the final balancing for the overruns/underruns of contract quantities on the project that are a result of addressing field conditions not accounted for in the original plans. This Change Order also adds small signs to increase the safety of the roadway and adds an item to repair an existing crash cushion attenuator.

Adjusted Price = \$1,442,349.54

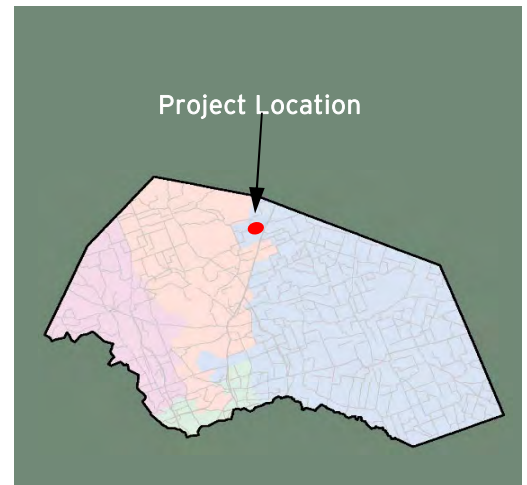

**Bud Stockton at FM 487 Traffic Signal  
(Intersection of Bud Stockton & FM 487)**

**Project Length: 1000 Feet  
Roadway Classification: Major Collector**

**Project Schedule: July 2024 - Late 2024  
Estimated Construction Cost: \$0.6M**



## **AUGUST 2024 IN REVIEW**

8/2/24: Subcontractor Myers Concrete continued excavating, forming, and pouring curb and sidewalk at corners of FM 487 and Bud Stockton intersection.

8/9/24: Subcontractor Myers Concrete continued excavating, forming, and pouring curb and sidewalk at corners of FM 487 and Bud Stockton intersection.

8/16/24: Subcontractor Myers Concrete began installing pedestrian handrail and detectable pavers in sidewalk curb ramps at the corners of the FM 487 and Bud Stockton intersection.

8/23/24: No work conducted on the project. Austin Traffic Signal awaiting signal materials.

8/30/24: No work performed on the project. Austin Traffic Signal awaiting signal materials.



Design Engineer: Kimley Horn  
Contractor: Austin Traffic Signal  
Construction Observation:  
Joseph Jones, HNTB

Williamson County  
Road Bond Program

**Project Name: Bud Stockton at FM 487 Traffic Signal**

**Project No. 24IFB33**

Original Contract Price = \$553,983.00

<u>Letting</u>	<u>Award</u>	<u>Notice To Proceed</u>	<u>Begin Work</u>	<u>Substantial Completion</u>	<u>Completion Certificate</u>	<u>Total Bid Days</u>	<u>Days Added</u>	<u>Total Days</u>
3/14/2024	4/25/2024	7/12/2024	7/22/2024			263		263

8/31/2024      Comments - The Contractor excavated, formed, and poured curb and sidewalk at the corners of the FM 487 and Bud Stockton intersection. The Contractor installed pedestrian handrail and detectable pavers at the ADA ramps at the corners of the FM 487 and Bud Stockton intersection. The Contractor is waiting on signal materials.

Adjusted Price = \$553,983.00
